



**Agreement No. CE 59/2020 (EP)  
Environmental Monitoring and  
Audit for Disposal Facility to the  
East of Sha Chau (2021-2026)  
– Investigation**

Monthly EM&A Report for  
Contaminated Mud Pits to the East of Sha Chau  
– February 2023

March 2023

Mott MacDonald  
3/F Manulife Place  
348 Kwun Tong Road  
Kwun Tong  
Kowloon  
Hong Kong

T +852 2828 5757  
mottmac.hk

Civil Engineering and  
Development Department  
Fill Management Division  
5/F, Civil Engineering and  
Development Building  
101 Princess Margaret  
Road  
Homantin, Kowloon

# **Agreement No. CE 59/2020 (EP) Environmental Monitoring and Audit for Disposal Facility to the East of Sha Chau (2021-2026) – Investigation**

Monthly EM&A Report for  
Contaminated Mud Pits to the East of Sha Chau  
– February 2023

March 2023

**Dredging, Management and Capping of Contaminated Sediment Disposal**

**Facility at Sha Chau**

**Environmental Certification Sheet**

**Environmental Permit No. EP-312/2008/A**

**Reference Document /Plan**

|                                                                  |                                                                                       |
|------------------------------------------------------------------|---------------------------------------------------------------------------------------|
| Document/ <del>Plan</del> to be <del>Certified</del> / Verified: | Monthly EM&A Report for Contaminated Mud Pits to the East of Sha Chau – February 2023 |
| Date of Report:                                                  | 8 March 2023                                                                          |
| Date prepared by ET:                                             | 8 March 2023                                                                          |
| Date received by IA:                                             | 8 March 2023                                                                          |

**Reference EP Condition**

Environmental Permit Condition:

Condition 3.4 of EP-312/2008/A:

4 hard copies and 1 electronic copy of monthly EM&A Report shall be submitted to the Director within 10 working days after the end of the reporting month. The EM&A Reports shall include a summary of all non-compliance (exceedances) of the environmental quality performance limits (Action and Limit Levels). The submissions shall be verified by the Independent Auditor. Additional copies of the submission shall be provided to the Director upon request by the Director.

**ET Certification**

I hereby certify that the above referenced document/~~plan~~ complies with the above referenced condition of EP-312/2008/A.

Ir Thomas Chan,  
Environmental Team Leader (ETL): 

Date: 8 March 2023

**IA Verification**

I hereby verify that the above referenced document/~~plan~~ complies with the above referenced condition of EP-312/2008/A.

Dr Wang Wen Xiong,  
Independent Auditor (IA): 

Date: 8 March 2023

# Issue and Revision Record

| Revision | Date     | Originator | Checker     | Approver   | Description                       |
|----------|----------|------------|-------------|------------|-----------------------------------|
| A        | Mar 2023 | Various    | Thomas Chan | Eric Ching | Revision A of Submission          |
| B        | Mar 2023 | Various    | Thomas Chan | Eric Ching | Revision B for Record [Finalised] |
|          |          |            |             |            |                                   |
|          |          |            |             |            |                                   |
|          |          |            |             |            |                                   |
|          |          |            |             |            |                                   |
|          |          |            |             |            |                                   |

**Document reference:** 423134 | 06/05/23 | B

**Information class:** Standard

This document is issued for the party which commissioned it and for specific purposes connected with the above-captioned project only. It should not be relied upon by any other party or used for any other purpose.

We accept no responsibility for the consequences of this document being relied upon by any other party, or being used for any other purpose, or containing any error or omission which is due to an error or omission in data supplied to us by other parties.

This document contains confidential information and proprietary intellectual property. It should not be shown to other parties without consent from us and from the party which commissioned it.

# Contents

|          |                                                                     |          |
|----------|---------------------------------------------------------------------|----------|
| <b>1</b> | <b>Introduction</b>                                                 | <b>1</b> |
| 1.1      | Background                                                          | 1        |
| 1.2      | Reporting Period                                                    | 2        |
| 1.3      | Details of Sampling and Laboratory Testing Activities               | 2        |
| 1.4      | Details of Outstanding Sampling or Analysis                         | 2        |
| <b>2</b> | <b>Brief Discussion of Monitoring Results for ESC CMP V</b>         | <b>3</b> |
| 2.1      | Introduction                                                        | 3        |
| 2.2      | Water Column Profiling of ESC CMP Vb – in February 2023             | 3        |
| 2.2.1    | In-situ Measurements                                                | 3        |
| 2.2.2    | Laboratory Measurements for Suspended Solids (SS)                   | 3        |
| 2.3      | Routine Water Quality Monitoring of ESC CMPs – in February 2023     | 3        |
| 2.3.1    | In-situ Measurements                                                | 4        |
| 2.3.2    | Laboratory Measurements                                             | 4        |
| 2.4      | Pit Specific Sediment Chemistry of ESC CMP Vb – in February 2023    | 4        |
| 2.5      | Cumulative Impact Sediment Chemistry of ESC CMPs – in February 2023 | 5        |
| <b>3</b> | <b>Future Key Issues</b>                                            | <b>6</b> |
| 3.1      | Activities Scheduled for the Next Reporting Period                  | 6        |
| 3.2      | Study Programme                                                     | 6        |

## Tables

|           |                              |
|-----------|------------------------------|
| Table 1.1 | Works Schedule for ESC CMP V |
|-----------|------------------------------|

## Figures

|            |                                                                           |
|------------|---------------------------------------------------------------------------|
| Figure 2.1 | Routine & Capping Water Quality Sampling Stations (Ebb-Tide) for ESC CMPs |
| Figure 2.2 | Pit Specific Sediment Quality Monitoring Stations for CMP V               |
| Figure 2.3 | Cumulative Impacts Sediment Quality Monitoring Stations for ESC CMPs      |

## Appendices

- Appendix A    Sampling Schedule
- Appendix B    Water Quality Monitoring Results
- Appendix C    Graphical Presentations
- Appendix D    Study Programme

# 1 Introduction

## 1.1 Background

The Civil Engineering and Development Department (CEDD) is managing a number of marine disposal facilities in Hong Kong waters, including the Contaminated Mud Pits (CMPs) to the East of Sha Chau (ESC) for the disposal of contaminated sediment, and various open-sea disposal grounds located to the South of Cheung Chau (SCC), East of Tung Lung Chau (ETLC) and East of Ninepins (ENP) for the disposal of uncontaminated sediment.

Environmental Permits (EPs) (Ref. No. EP-312/2008/A) was issued by the Environmental Protection Department (EPD) to the CEDD, the Permit Holder, on 28 November 2008 for the Project - Disposal of Contaminated Sediment – Dredging, Management and Capping of Sediment Disposal Facility at Sha Chau.

Under the requirements of the EP, EM&A programmes which encompass water and sediment chemistry, fisheries assessment, tissue and whole body analysis, sediment toxicity and benthic recolonisation studies as set out in the EM&A Manuals are required to be implemented. EM&A programmes have been continuously carried out during the operation of the CMPs at ESC. A review of the collection and analysis of such environmental data from the monitoring programme demonstrated that there had not been any adverse environmental impacts resulting from disposal activities.<sup>1,2</sup> The current programme will assess the impacts resulting from dredging, disposal and capping operations of CMP V.

A proposal on the change of number of sample replication of water quality and sediment monitoring as well as combination of routine water quality monitoring and water quality monitoring during capping operation was submitted to EPD and agreed by EPD on 3 December 2020. The proposed changes have been effective for the EM&A activities since December 2020. In early 2022, after implementing the Phase 1 optimisation for at least one year, a further data review was conducted. The monitoring data has been reviewed and demonstrated that the data robustness and representativeness are maintained. Therefore, a technical note presenting the data review results served as a supplementary information was submitted to EPD and presented that Phase 2 optimization of sample replication of water quality and sediment monitoring for the Project will be implemented in 2022. EPD expressed no comment on the review and note the implementation of Phase 2 optimization of sample replication on 18 May 2022, and thus this optimization has been effective for the EM&A activities since July 2022.

The latest sampling schedule is provided in **Appendix A**.

The present EM&A programme under Agreement No. CE 59/2020 (EP) covers the dredging, disposal and capping operations of the ESC CMP V (see **Appendix A** for the EM&A programme.) Detailed works schedule for ESC CMP V is shown in **Table 1.1**. In February 2023, the following works were undertaken:

- Disposal of contaminated mud at ESC CMP Vb; and
- Capping operations at ESC CMP Vd.

---

<sup>1</sup> ERM (2013) Final Report. Submitted under Agreement No. CE 4/2009 (EP) Environmental Monitoring and Audit for Contaminated Mud Pit at East Sha Chau. For CEDD.

<sup>2</sup> ERM (2017) Final Report. Submitted under Agreement No. CE 23/2012 (EP) Environmental Monitoring and Audit for Contaminated Mud Pits to the South of The Brothers and at East Sha Chau (2012 - 2017). For CEDD.

[illegible]



## 2 Brief Discussion of Monitoring Results for ESC CMP V

### 2.1 Introduction

This section presents a brief discussion of the results obtained from the following monitoring activities for ESC CMP V during the reporting period:

- Water Column Profiling of ESC CMP Vb;
- Routine Water Quality Monitoring of ESC CMPs;
- Pit Specific Sediment Chemistry of ESC CMP Vb; and
- Cumulative Impact Sediment Chemistry of ESC CMPs.

### 2.2 Water Column Profiling of ESC CMP Vb – in February 2023

Water Column Profiling was undertaken at a total of two sampling stations (Upstream and Downstream stations) on 7 February 2023. The monitoring results have been assessed for compliance with the Water Quality Objectives (WQOs) set by Environmental Protection Department (EPD). This consists of a review of the EPD routine water quality monitoring data for the wet season period (November to March) of 2012 – 2021 from stations in the North Western Water Control Zone (WCZ), where the ESC CMPs are located.<sup>3</sup> For Salinity, the averaged value obtained from the Reference (Upstream) station was used for the basis as the WQO. Levels of Dissolved Oxygen (DO) and Turbidity were also assessed for compliance with the Action and Limit Levels (see **Table B1** of **Appendix B** for details).

#### 2.2.1 In-situ Measurements

Analyses of results for February 2023 indicated that levels of Salinity, pH and DO complied with the WQOs at both Downstream and Upstream stations (**Table B2** of **Appendix B**). Levels of DO and Turbidity at all stations complied with the Action and Limit Levels (**Tables B1 and B2** of **Appendix B**).

#### 2.2.2 Laboratory Measurements for Suspended Solids (SS)

Analyses of results for February 2023 indicated that the SS level at both Downstream and Upstream stations complied with the WQO and the Action and Limit Levels (**Tables B1 and B2** of **Appendix B**).

Overall, the monitoring results indicated that the mud disposal operation at ESC CMP Vb did not appear to cause any deterioration in water quality during this reporting period.

### 2.3 Routine Water Quality Monitoring of ESC CMPs – in February 2023

Routine Water Quality Monitoring of ESC CMPs was undertaken on 6 February 2023. The monitoring results have been assessed for compliance with the WQOs (see **Section 2.2** above for details). The monitoring results are shown in **Tables B3, B4 and B5** of **Appendix B** and **Figures 1 to 11** of **Appendix C**. A total of sixteen (16) monitoring stations were sampled in February 2023 as shown in **Figure 2.1**.

---

<sup>3</sup> <http://epic.epd.gov.hk/EPICRIVER/marine/?lang=en>

### 2.3.1 In-situ Measurements

Graphical presentation of the monitoring results (Temperature, DO, pH, Salinity and Turbidity) is shown in **Figures 1 to 6 of Appendix C**. Analyses of results indicated that the levels of pH, Salinities and DO complied with the WQOs at all stations in February 2023. The levels of DO and Turbidity complied with the Action and Limit Levels at all stations (**Table B3 of Appendix B; Figures 3 and 6 of Appendix C**).

Overall, *in-situ* measurement results of the Routine Water Quality Monitoring indicated that the disposal and capping operation at ESC CMPs did not appear to cause any unacceptable impacts in water quality in February 2023.

### 2.3.2 Laboratory Measurements

Laboratory analysis of samples obtained during the reporting period indicated that the concentrations of Arsenic, Cadmium, Chromium, Copper, Mercury, Nickel and Zinc were detected in the samples at some / all stations and their concentrations were generally similar across stations; except the concentrations of Arsenic and Zinc were slightly higher at Ma Wan (MW1) station; and the concentrations of Chromium was higher at Reference (RFE) Stations. (**Table B4 of Appendix B; Figure 7 and 8 of Appendix C**).

For nutrients, concentrations of Total Inorganic Nitrogen (TIN) were similar across all stations. (**Table B5 of Appendix B; Figure 9 of Appendix C**). The concentration of Ammonia Nitrogen (NH<sub>3</sub>-N) was slightly higher at Ma Wan (MW1) station (**Table B5 of Appendix B; Figure 9 of Appendix C**). The concentrations of Biochemical Oxygen Demand (BOD<sub>5</sub>) was higher at Intermediate (INE) station. (**Table B5 of Appendix B; Figure 10 of Appendix C**).

Analyses of results for the reporting period indicated that the SS levels complied with the dry season WQO (13.0 mg/L) and the Action and Limit Levels at all stations. (**Tables B1 and B5 of Appendix B; Figure 11 of Appendix C**).

Based on the available results of the Routine Water Quality Monitoring which indicated that the disposal and capping operation at ESC CMPs did not appear to cause any unacceptable deterioration in water quality during the reporting period. Detailed statistical analysis will be presented in the Quarterly EM&A Report to investigate any spatial and temporal trends of potential concern.

## 2.4 Pit Specific Sediment Chemistry of ESC CMP Vb – in February 2023

Monitoring locations for Pit Specific Sediment Chemistry for ESC CMP Vb are shown in **Figure 2.2**. A total of six (6) monitoring stations were sampled on 1 February 2023.

The concentrations of most inorganic contaminants were lower than the Lower Chemical Exceedance Levels (LCELs) at all stations, except for Arsenic. The concentrations of Arsenic were higher than the LCEL at Near-Pit station ESC-NNCA, Pit-Edge station ESC-NECA, and Active-Pit stations ESC-NPCA (**Figures 12 and 13 of Appendix C**).

Whilst the average concentration of Arsenic in the Earth's crust is generally ~2mg/kg, significantly higher Arsenic concentrations (median = 14 mg/kg) have been recorded in Hong Kong's onshore sediments.<sup>4</sup> It is presumed that the natural concentrations of Arsenic are similar in onshore and offshore sediments,<sup>5</sup> and relatively high Arsenic levels may thus occur throughout Hong Kong.

<sup>4</sup> Sewell RJ (1999) Geochemical Atlas of Hong Kong. Geotechnical Engineering Office, Government of the Hong Kong Special Administrative Region

<sup>5</sup> Whiteside PGD (2000) Natural geochemistry and contamination of marine sediments in Hong Kong. In: The Urban Geology of Hong Kong (ed. Page A & Reels SJ). Geological Society of Hong Kong Bulletin No. 6, p109-121

Therefore, the LCEL exceedances of Arsenic are unlikely to be caused by the disposal operations at ESC CMP Vb but rather as a result of naturally occurring deposits.

For organic contaminants, the concentrations of Total Organic Carbon (TOC) were higher at Active-Pit station ESC-NPCB. (**Figure 14 of Appendix C**). The concentrations of Low Molecular Weight Polycyclic Aromatic Hydrocarbons (PAHs) were higher than UCEL (Upper Chemical Exceedance Level) at Active-Pit stations ESC-NPCA and ESC-NPCB.

For High Molecular Weight Polycyclic Aromatic Hydrocarbons (PAHs), the concentrations were higher than UCEL at Active-Pit station ESC-NPCA and ESC-NPCB. (**Figures 15a and 15b of Appendix C**). The concentrations of Tributyltin (TBT), Total Polychlorinated Biphenyls (PCBs), Total dichloro-diphenyl-trichloroethane (DDT) and 4,4'-dichlorodiphenyldichloroethylene (DDE) were below the limit of reporting at all stations during the reporting period.

Considering that the higher levels of Low Molecular Weight and High Molecular Weight PAHs occurred within Active-Pit stations ESC-NPCA and ESC-NPCB only, there is no evidence indicating any unacceptable environmental impacts to sediment quality outside the pit area as a result of the contaminated mud disposal operations at ESC CMP Vb during the reporting period.

Statistical analysis will be undertaken and presented in the corresponding Quarterly EM&A Report to investigate whether there are any unacceptable impacts in the area caused by the contaminated mud disposal.

## 2.5 Cumulative Impact Sediment Chemistry of ESC CMPs – in February 2023

Monitoring locations for Cumulative Impact Sediment Chemistry for ESC CMPs are shown in **Figure 2.3**. A total of nine (9) monitoring stations were sampled on 2 February 2023.

Analyses of results for the Cumulative Impact Sediment Chemistry Monitoring indicated that the concentrations of most inorganic contaminants were below the LCEL at most stations during the reporting period, except concentrations of Arsenic were higher than the LCEL at Near-field stations ESC-RNA, ESC-RNB1, Mid-field stations ESC-RMA, ESC-RMB, Far-field stations ESC-RFA, ESC-RFB and Ma Wan station MW1 (**Figures 16 and 17 of Appendix C**). As discussed in **Section 2.4**, the LCEL exceedances of Arsenic are unlikely to be caused by the disposal operations at ESC CMP Vb but rather as a result of naturally occurring deposits.

For organic contaminants, the concentration of TOC was higher at Capped Pit station ESC-RCA1 (**Figure 18 of Appendix C**). The concentrations of High Molecular Weight PAHs were higher at Capped Pit station ESC-RCB1, while the concentrations of Low Molecular Weight PAHs were similar across stations. (**Figure 19 of Appendix C**)

The concentrations of TBT were higher at Ma Wan station MW1 (**Figure 20 of Appendix C**). The concentrations of Total PCBs, Total DDT, 4,4'-DDE, 2,4'-DDT, 4,4'-DDT were below the limit of reporting at all stations during the reporting period.

Overall, there is no evidence indicating any unacceptable environmental impacts to sediment quality as a result of the contaminated mud disposal operations at ESC CMP Vb during the reporting period. Statistical analysis will be undertaken and presented in the corresponding Quarterly EM&A Report to investigate whether there are any unacceptable impacts in the area caused by the contaminated mud disposal.

## 3 Future Key Issues

### 3.1 Activities Scheduled for the Next Reporting Period


The following monitoring activities will be conducted in the next reporting period of March 2023 for ESC CMP V (see **Appendix A** for the sampling schedule):

- Water Column Profiling of ESC CMP Vb;
- Routine Water Quality Monitoring of ESC CMPs; and
- Pit Specific Sediment Chemistry of ESC CMP Vb.

### 3.2 Study Programme

A summary of the Study Programme is presented in **Appendix D**.

# Figures

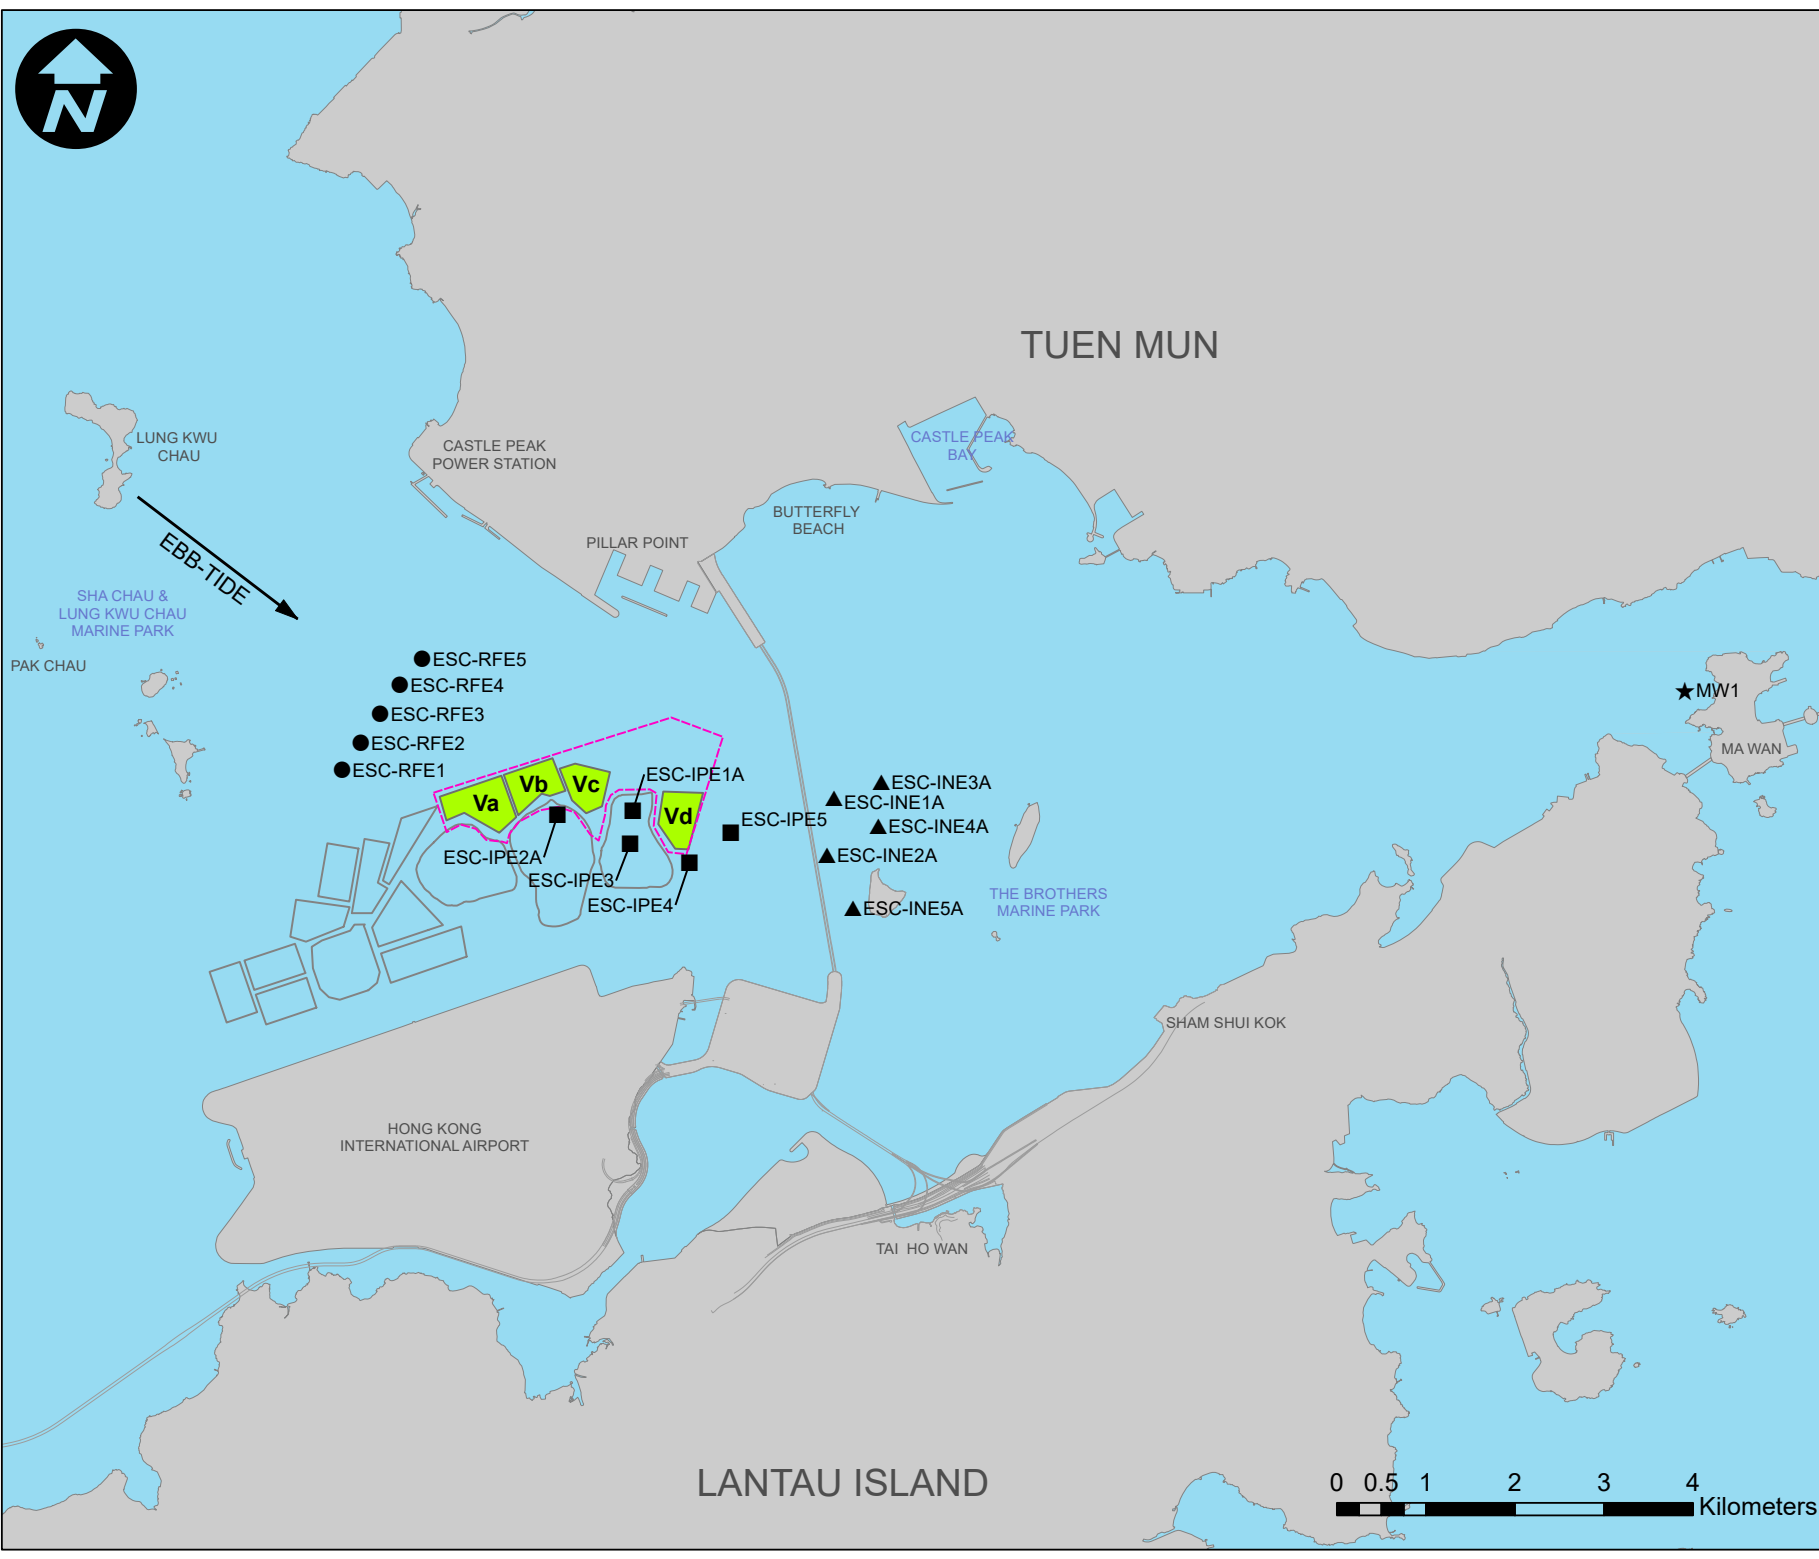

Notes:

Key to symbols:

## LEGEND

ESC CMP V

ESC USABLE AREA 1

### WATER QUALITY SAMPLING STATIONS

IMPACT STATION

INTERMEDIATE STATION

REFERENCE STATION

MA WAN STATION

|     |          |       |             |        |       |
|-----|----------|-------|-------------|--------|-------|
|     |          |       |             |        |       |
| P1  | APR 2021 | KN    |             |        |       |
| Rev | Date     | Drawn | Description | Ch'k'd | App'd |

**MOTT MACDONALD**

3/F International Trade Tower  
348 Kwun Tong Road  
Kwun Tong, Kowloon  
Hong Kong  
T +852 2828 5757  
F +852 2821823  
W mottmac.com

Client


**CEDD** 土木工程拓展署  
Civil Engineering and Development Department

Project **AGREEMENT NO. CE 59/2020 (EP)  
ENVIRONMENTAL MONITORING AND AUDIT  
FOR DISPOSAL FACILITY  
TO THE EAST OF SHA CHAU (2021-2026)  
- INVESTIGATION**

Title **ROUTINE & CAPPING WATER QUALITY  
SAMPLING STATIONS (EBB-TIDE)  
FOR ESC CMPS**

|             |        |              |  |
|-------------|--------|--------------|--|
| Designed    |        | Eng check    |  |
| Drawn       |        | Coordination |  |
| Dwg check   |        | Approved     |  |
| Scale at A3 | Status | Rev          |  |

Drawing Number **FIGURE 2.1**

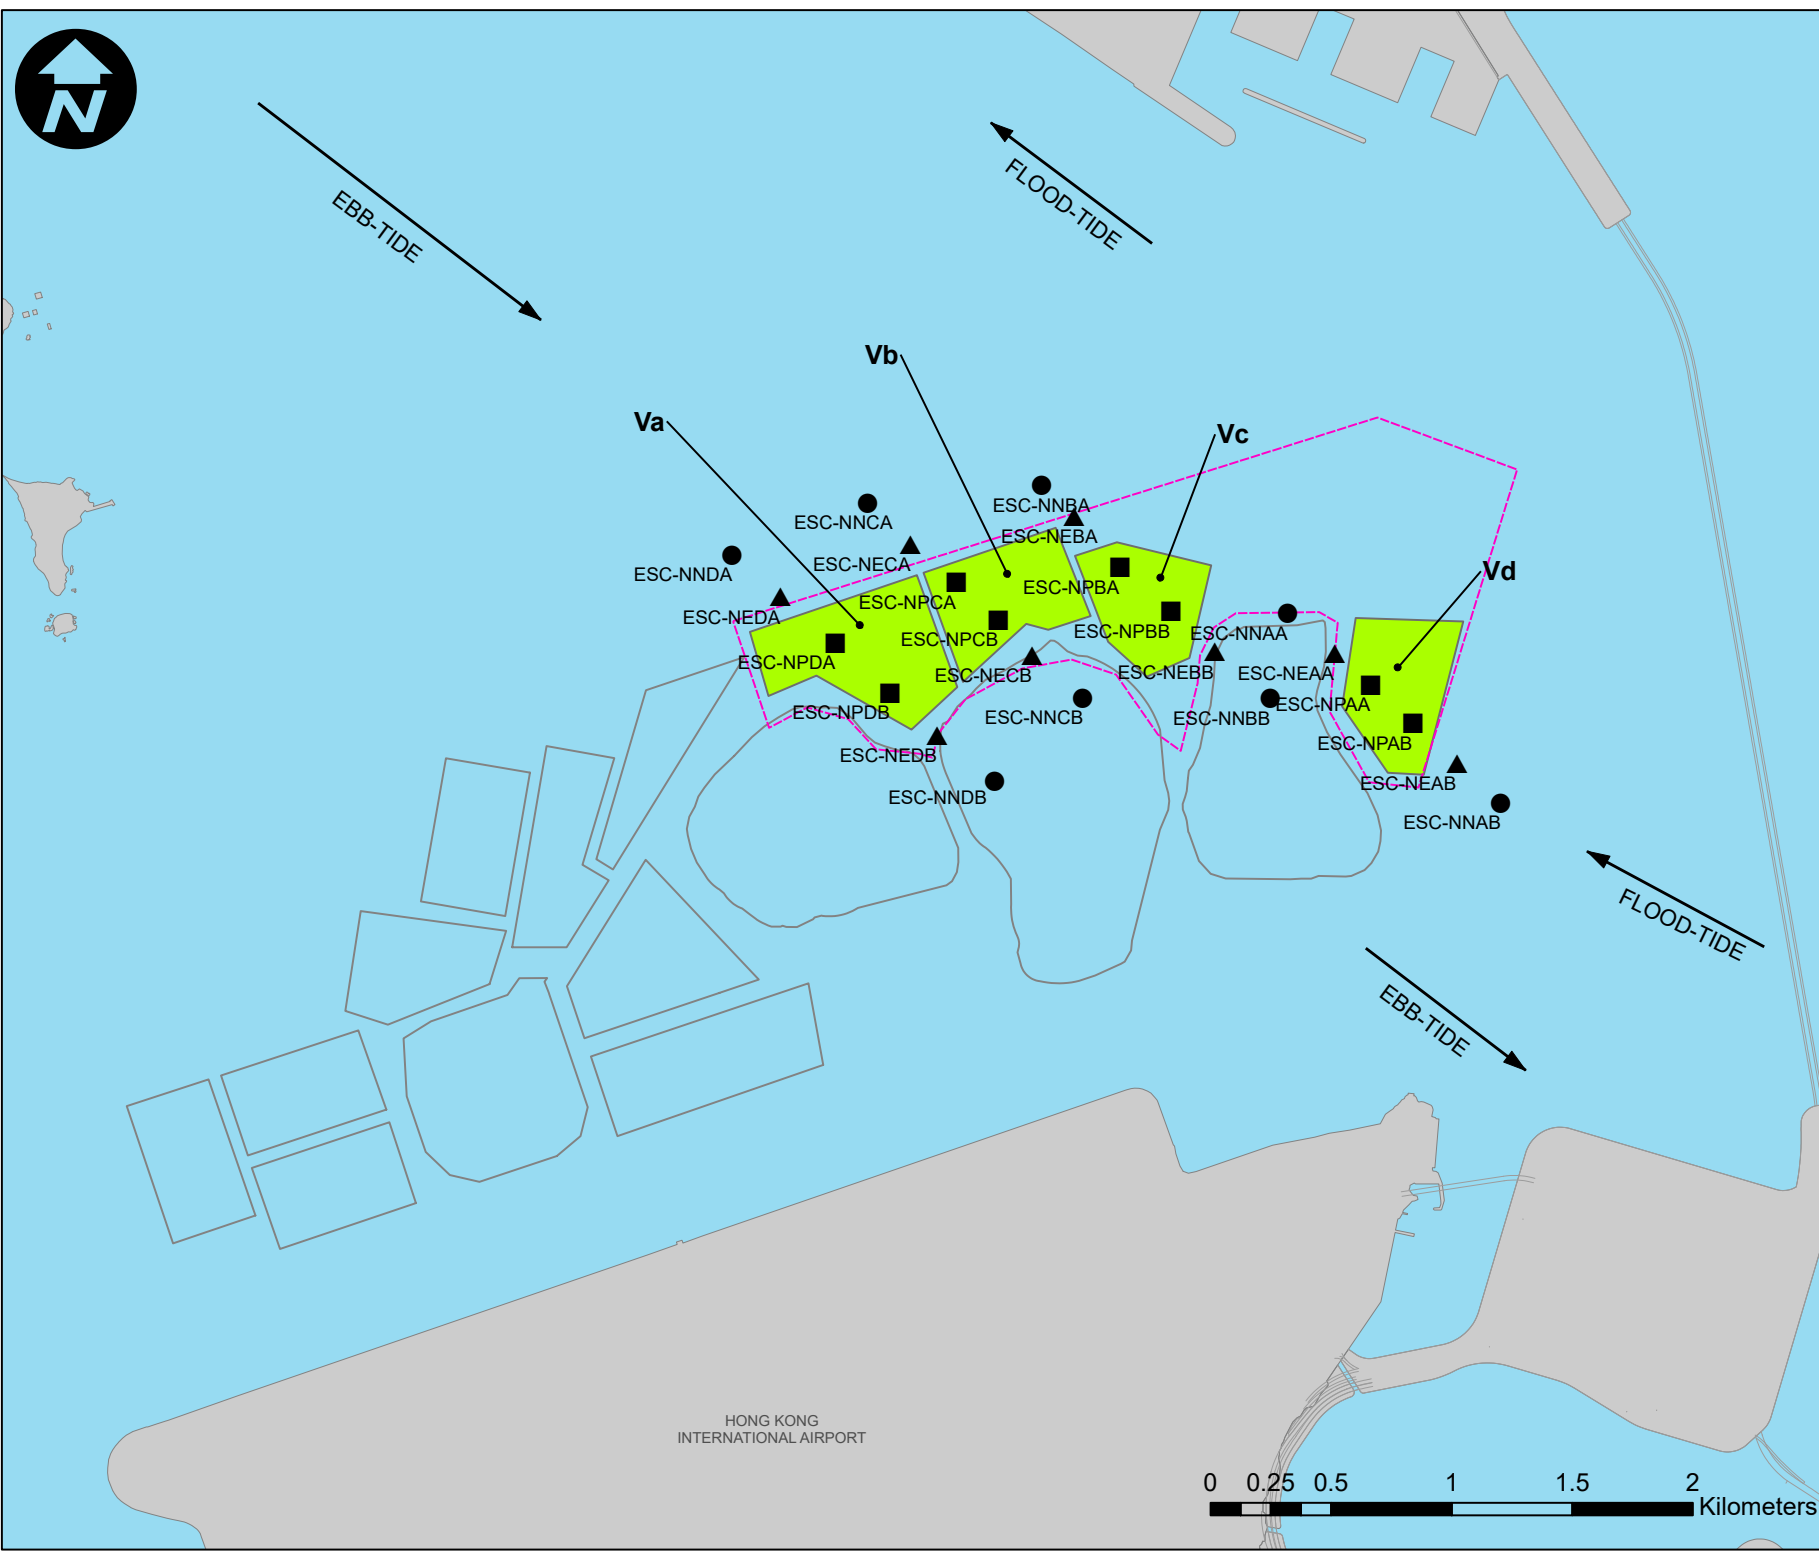

Key Plan:

Notes:

Key to symbols:

**LEGEND**

- ESC CMP V
- ESC USABLE AREA 1

**PIT SPECIFIC SEDIMENT MONITORING STATIONS**

- ACTIVE-PIT STATION
- PIT-EDGE STATION
- NEAR-PIT STATION

|     |          |       |             |        |       |
|-----|----------|-------|-------------|--------|-------|
|     |          |       |             |        |       |
|     |          |       |             |        |       |
| P1  | APR 2021 | KN    |             |        |       |
| Rev | Date     | Drawn | Description | Ch'k'd | App'd |

**M**

**MOTT**

**MACDONALD**

3/F International Trade Tower  
348 Kwun Tong Road  
Kwun Tong, Kowloon  
Hong Kong  
T +852 2828 5757  
F +852 2821823  
W mottmac.com

Client

**CEDD**

土木工程拓展署  
Civil Engineering and  
Development Department

Project

**AGREEMENT NO. CE 59/2020 (EP)  
ENVIRONMENTAL MONITORING AND AUDIT  
FOR DISPOSAL FACILITY  
TO THE EAST OF SHA CHAU (2021-2026)  
- INVESTIGATION**



Title

**PIT SPECIFIC SEDIMENT QUALITY  
MONITORING STATIONS FOR CMP V**

|             |  |        |              |     |  |
|-------------|--|--------|--------------|-----|--|
| Designed    |  |        | Eng check    |     |  |
| Drawn       |  |        | Coordination |     |  |
| Dwg check   |  |        | Approved     |     |  |
| Scale at A3 |  | Status |              | Rev |  |

Drawing Number

**FIGURE 2.2**

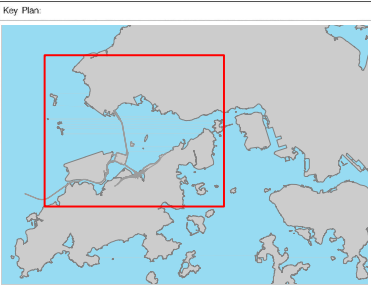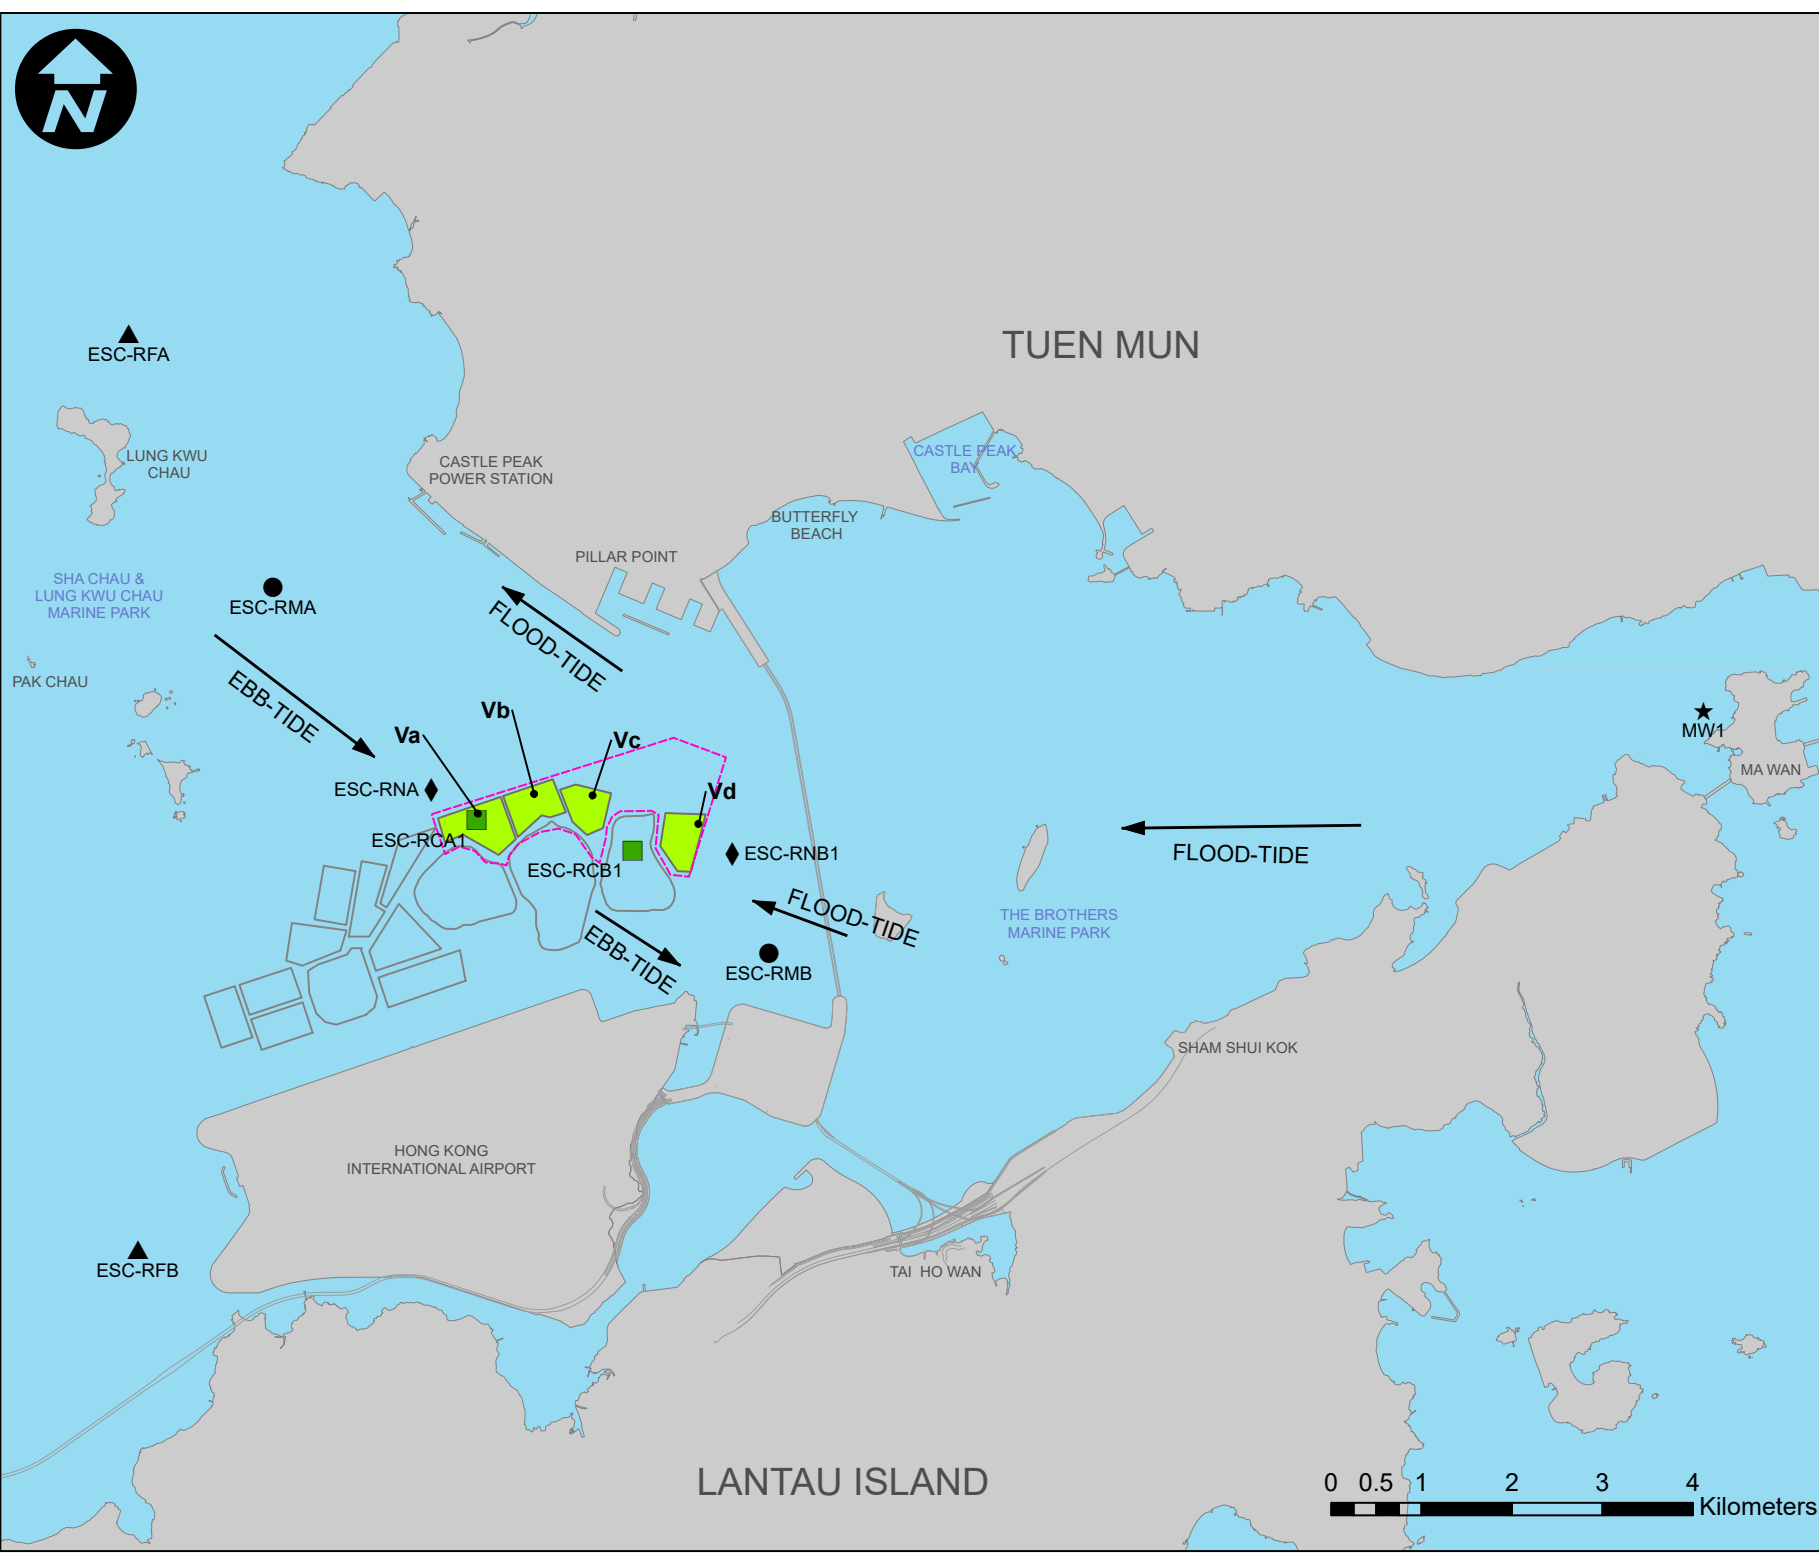

Notes:

Key to symbols:

### LEGEND

- ESC CMP V
- ESC USABLE AREA 1

### CUMULATIVE IMPACT SEDIMENT MONITORING STATIONS

- CAPPED PIT STATION
- NEAR-FIELD STATION
- MID-FIELD STATION
- FAR-FIELD STATION
- MA WAN STATION

|     |          |       |             |        |       |
|-----|----------|-------|-------------|--------|-------|
|     |          |       |             |        |       |
| P1  | APR 2021 | KN    |             |        |       |
| Rev | Date     | Drawn | Description | Ch'k'd | App'd |

**MOTT MACDONALD**

3/F International Trade Tower  
348 Kwun Tong Road  
Kwun Tong, Kowloon  
Hong Kong  
T +852 2828 5757  
F +852 2821823  
W mottmac.com

Client

**CEDD** 土木工程拓展署  
Civil Engineering and Development Department

Project **AGREEMENT NO. CE 59/2020 (EP) ENVIRONMENTAL MONITORING AND AUDIT FOR DISPOSAL FACILITY TO THE EAST OF SHA CHAU (2021-2026) – INVESTIGATION**

Title **CUMULATIVE IMPACTS SEDIMENT QUALITY MONITORING STATIONS FOR ESC CMPS**

|                |            |              |  |  |
|----------------|------------|--------------|--|--|
| Designed       |            | Eng check    |  |  |
| Drawn          |            | Coordination |  |  |
| Dwg check      |            | Approved     |  |  |
| Scale at A3    | Status     | Rev          |  |  |
| Drawing Number | FIGURE 2.3 |              |  |  |



# Appendices

|            |                                  |
|------------|----------------------------------|
| Appendix A | Sampling Schedule                |
| Appendix B | Water Quality Monitoring Results |
| Appendix C | Graphical Presentations          |
| Appendix D | Study Programme                  |

## Appendix A. Sampling Schedule

**East of Sha Chau CMPs**  
**Environmental Monitoring and Audit Sampling Schedule**  
**(January 2021 - March 2026)**

[illegible]

(1) The number shown in each cell represents the numbers of replicates per monitoring station. The number shown in **green bolded text** represented monitoring works have been conducted before/ during the reporting period of this Monthly EM&A Report, while the number shown in black represent planned monitoring works after the reporting period of this Monthly EM&A Report.

(2) For the planned Routine Water Quality Monitoring (i.e. the numbers of replicates per monitoring station shown in black), the monitoring will be conducted at mid-ebb OR mid-flood tide. The yearly tidal selection of this monitoring will be based on a principle to obtain 6 months monitoring data at mid-ebb, and 6 months monitoring data at mid-flood.

(3) Impact Monitoring for Dredging will be scheduled when dredging operations commence.

(4) Benthic Recolonisation Studies for CMP V will be scheduled when capping operation for CMP V is completed.

Remarks:

A proposal on the change of number of sample replication of water quality & sediment monitoring and combination of routine water quality monitoring and water quality monitoring during capping operation was submitted to EPD and agreed by EPD on 3 December 2020. The proposed changes have been implemented for the EM&A activities since December 2020. Water Quality Monitoring during Capping Operation and Routine Water Quality Monitoring are combined such that Routine Water Quality Monitoring have been conducted monthly starting in December 2020. A technical note presenting the data review results served as a supplementary information was submitted to EPD and presented that Phase 2 optimization of sample replication of water quality and sediment monitoring for the Project will be implemented in 2022 was provided to EPD in April 2022. Phase 2 optimization of sample replication has been effective for the EM&A activities since July 2022.

# Due to the logistic problem induced by the pandemic which adversely affecting the supply of international species adopted in testing programme of Sediment Toxicity Tests, as such, Sediment Toxicity Tests of ESC CMPs originally scheduled in February 2022 were postponed to March 2022.

<sup>A</sup> To enable the required Research Fishing Permit could be granted by the time undertaking the Demersal Trawling, trawling originally scheduled in July and August 2022 was postponed to August and September 2022.

## **Appendix B. Water Quality Monitoring Results**

**Table B1: Action and Limit Levels of Water Quality for Dredging, Disposal and Capping Activities at ESC CMP V**

| Parameters                                                                            | Action                                                                                                                                                                                                                   | Limit                                                                                                                                                                                                                                   |
|---------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Dissolved Oxygen (DO) in mg L <sup>-1</sup> (Surface, Middle & Bottom) <sup>(1)</sup> | <b>Surface and Middle Depth<sup>(2)</sup></b><br>5%-ile of baseline data for surface and middle layer = <b>3.76</b><br>and<br>Significantly less than the reference station's mean DO (at the same tide of the same day) | <b>Surface and Middle Depth<sup>(2)</sup></b><br>1%-ile of baseline data for surface and middle layer = <b>3.11</b> <sup>(3)</sup><br>and<br>Significantly less than the reference station's mean DO (at the same tide of the same day) |
|                                                                                       | <b>Bottom</b><br>5%-ile of baseline data for surface and middle layer = <b>2.96</b><br>and<br>Significantly less than the reference station's mean DO (at the same tide of the same day)                                 | <b>Bottom</b><br>The average of the impact station readings are <b>&lt; 2</b><br>and<br>Significantly less than the reference station's mean DO (at the same tide of the same day)                                                      |
| Suspended Solids (SS) in mg L <sup>-1</sup> (depth-averaged) <sup>(5)</sup>           | 95%-ile of baseline data for depth-averaged = <b>37.88</b><br>and<br>120% of control station's SS at the same tide of the same day                                                                                       | 99%-ile of baseline data for depth-averaged = <b>61.92</b><br>and<br>130% of control station's SS at the same tide of the same day                                                                                                      |
| Turbidity in NTU (depth-averaged) <sup>(4)(5)</sup>                                   | 95%-ile of baseline data = <b>28.14</b><br>and<br>120% of control station's Turbidity at the same tide of the same day                                                                                                   | 99%-ile of baseline data = <b>38.32</b><br>and<br>130% of control station's Turbidity at the same tide of the same day                                                                                                                  |

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. Action and Limit Levels for DO for Surface and Middle layers were calculated from the combined pool of baseline surface layer data and baseline middle layer data.
3. Given the Action Level for DO for Surface and Middle layers has already been lower than 4 mg L<sup>-1</sup>, it is proposed to set the Limit Level at 3.11 mg L<sup>-1</sup> which is the first percentile of the baseline data.
4. "Depth-averaged" is calculated by taking the arithmetic means of reading of all three depths.
5. For turbidity and SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.

**Table B2: Water Column Profiling Results for ESC CMP Vb in February 2023**

| Station               | Temp.<br>(°C) | Salinity<br>(ppt)        | Turbidity<br>(NTU) | Dissolved Oxygen<br>(%) | (mg L <sup>-1</sup> ) | pH      | Suspended Solids<br>(mg L <sup>-1</sup> ) |
|-----------------------|---------------|--------------------------|--------------------|-------------------------|-----------------------|---------|-------------------------------------------|
| WCP 1<br>(Downstream) | 18.26         | 31.25                    | 1.33               | 137.09                  | 10.71                 | 8.17    | 7.5                                       |
| WCP 2<br>(Upstream)   | 18.39         | 31.12                    | 1.77               | 138.16                  | 10.77                 | 8.15    | 4.0                                       |
| WQO<br>(Dry Season)   | N/A           | 28.01-34.24 <sup>#</sup> | N/A                | N/A                     | >4                    | 6.5-8.5 | 13.0                                      |

Notes:

1. <sup>#</sup> Not exceeding 10% of natural ambient level which is the result obtained from the Reference Station.
2. Cell shaded yellow / red indicates value exceeding the Action/Limit levels.
3. Cell shaded grey indicates value exceeding the WQO.

**Table B3: In-situ Monitoring Results for Routine Water Quality Monitoring of ESC CMPs in February 2023**

| Station            | Temp.<br>(°C) | Salinity<br>(ppt)        | Turbidity<br>(NTU) | Dissolved Oxygen<br>(%) | (mg L <sup>-1</sup> ) | pH      |
|--------------------|---------------|--------------------------|--------------------|-------------------------|-----------------------|---------|
| RFE (Reference)    | 17.95         | 31.87                    | 1.58               | 136.38                  | 10.68                 | 8.01    |
| IPE (Impact)       | 17.98         | 31.83                    | 1.68               | 136.64                  | 10.69                 | 8.09    |
| INE (Intermediate) | 17.98         | 32.24                    | 1.73               | 134.59                  | 10.51                 | 8.09    |
| Ma Wan             | 17.95         | 32.70                    | 0.94               | 125.02                  | 9.74                  | 7.97    |
| WQO (Dry Season)   | N/A           | 28.68-35.05 <sup>#</sup> | N/A                | N/A                     | >4                    | 6.5-8.5 |

Notes:

1. <sup>#</sup> Not exceeding 10% of natural ambient level which is the result obtained from the Reference Station.
2. Cell shaded yellow / red indicates value exceeding the Action/Limit levels.
3. Cell shaded grey indicates value exceeding the WQO.

**Table B4: Laboratory Results for Dissolved Metals and Metalloid in Routine Water Quality Monitoring of ESC CMPs in February 2023**

| Station | As<br>(µg/L) | Cd<br>(µg/L) | Cr<br>(µg/L) | Cu<br>(µg/L) | Pb<br>(µg/L) | Hg<br>(µg/L) | Ni<br>(µg/L) | Ag<br>(µg/L) | Zn<br>(µg/L) |
|---------|--------------|--------------|--------------|--------------|--------------|--------------|--------------|--------------|--------------|
| RFE     | 1.74         | 0.04         | 0.16         | 0.52         | ND           | 0.002        | 0.71         | ND           | 0.79         |
| IPE     | 1.53         | 0.03         | 0.13         | 0.48         | ND           | 0.001        | 0.65         | ND           | 0.07         |
| INE     | 1.57         | 0.03         | 0.12         | 0.53         | ND           | 0.002        | 0.59         | ND           | ND           |
| Ma Wan  | 2.01         | 0.03         | 0.09         | 0.42         | ND           | 0.002        | 0.53         | ND           | 1.70         |

Note:

1. "ND" indicates the concentrations of metals and metalloids are not detected.

**Table B5: Laboratory Results for Nutrients and Suspended Solid in Routine Water Quality Monitoring of ESC CMPs in February 2023**

| Station | NH <sub>3</sub><br>(mg/L) | TIN<br>(mg/L) | BOD <sub>5</sub><br>(mg/L) | SS<br>(mg/L) |
|---------|---------------------------|---------------|----------------------------|--------------|
| RFE     | 0.02                      | 0.13          | 1.88                       | 5.6          |
| IPE     | 0.03                      | 0.13          | 1.98                       | 5.5          |
| INE     | 0.02                      | 0.09          | 2.10                       | 5.2          |
| Ma Wan  | 0.07                      | 0.18          | 1.80                       | 4.5          |

WQO of TIN: 0.5 mg/L


Dry Season WQO of SS: 13.0 mg/L

Notes:


1. "<LOR" indicates the concentrations of contaminants are below the limit of reporting.
2. Cell shaded yellow / red indicates value exceeding the Action/Limit levels.
3. Cell shaded grey indicates value exceeding the WQO.

## Appendix C. Graphical Presentations



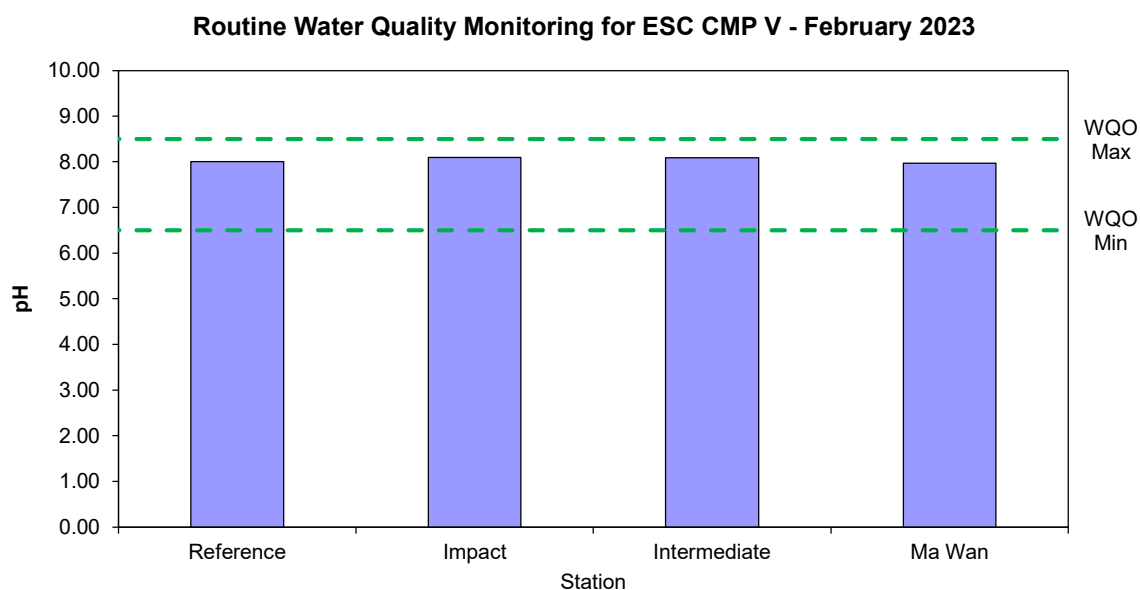


**Figure 1:** Level of pH recorded during Routine Water Quality Monitoring for disposal operations at ESC CMP V in February 2023

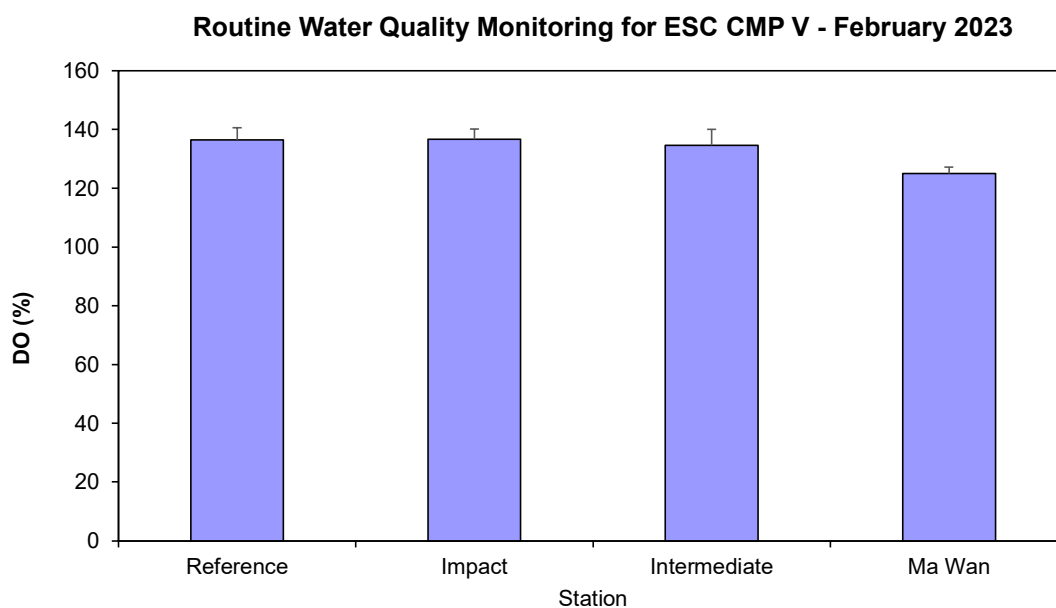


**Figure 2:** Level of Dissolved Oxygen (DO) (% saturation; mean + SD<sup>1</sup>) recorded during Routine Water Quality Monitoring for disposal operations at ESC CMP V in February 2023

<sup>1</sup> The mean and standard deviation (SD) for in-situ data are the mean and SD for water columns within the area.

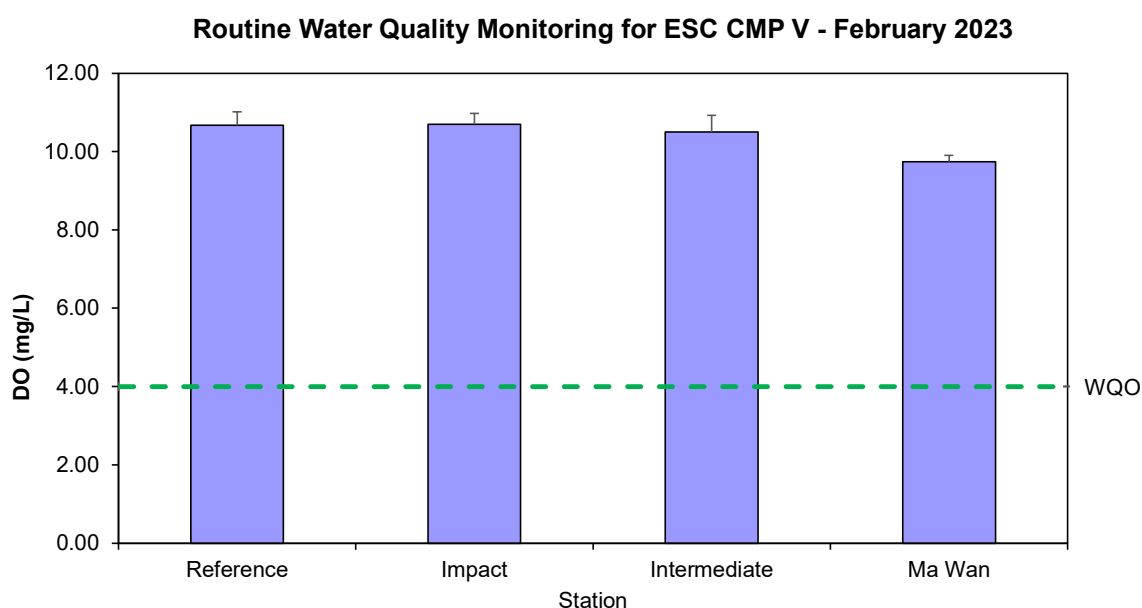


**Figure 3:** Concentration of Dissolved Oxygen (DO) (mg/L; mean + SD) recorded during Routine Water Quality Monitoring for disposal operations at ESC CMP V in February 2023

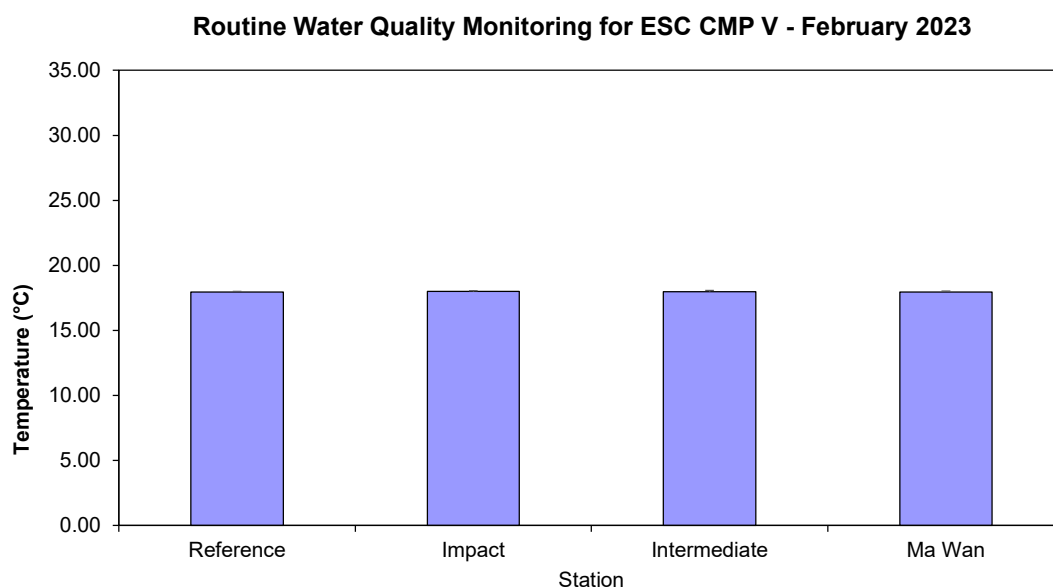


**Figure 4:** Level of Temperature (°C; mean + SD) recorded during Routine Water Quality Monitoring for disposal operations at ESC CMP V in February 2023

<sup>1</sup> The mean and standard deviation (SD) for in-situ data are the mean and SD for water columns within the area.

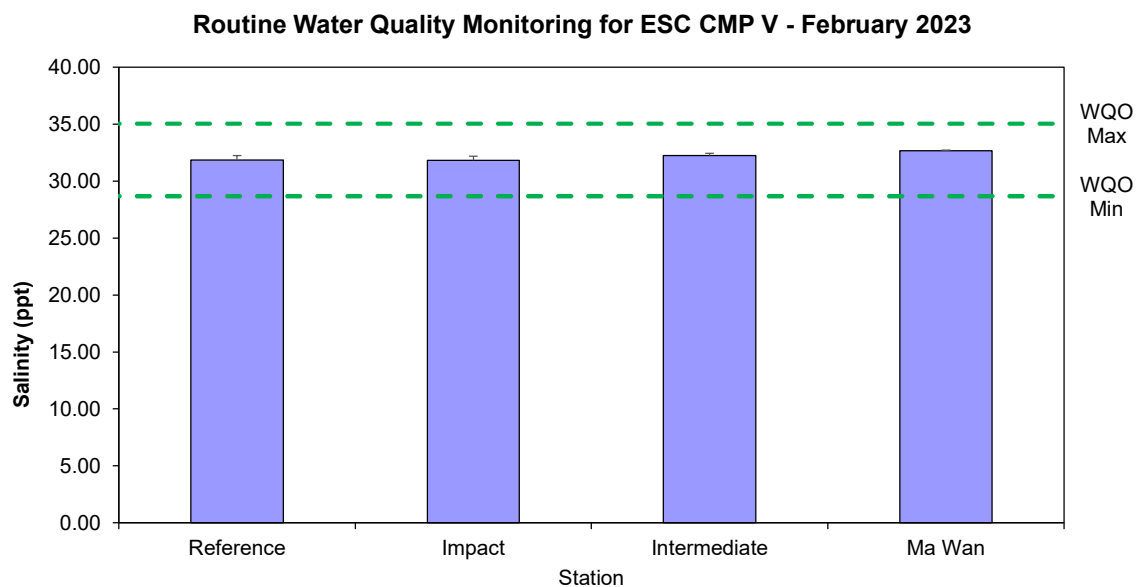


**Figure 5:** Level of Salinity (ppt; mean + SD<sup>1</sup>) recorded during Routine Water Quality Monitoring for disposal operations at ESC CMP V in February 2023

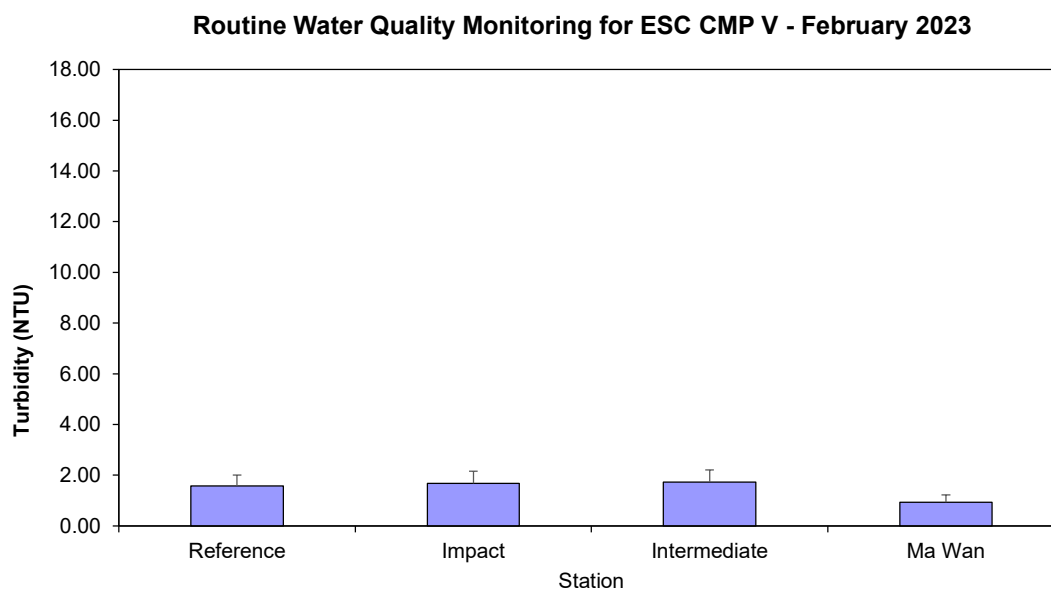

**Figure 6:** Level of Turbidity (NTU; mean + SD<sup>1</sup>) recorded during Routine Water Quality Monitoring for disposal operations at ESC CMP V in February 2023


<sup>1</sup> The mean and standard deviation (SD) for in-situ data are the mean and SD for water columns within the area.

### Routine Water Quality Monitoring for ESC CMP V February 2023

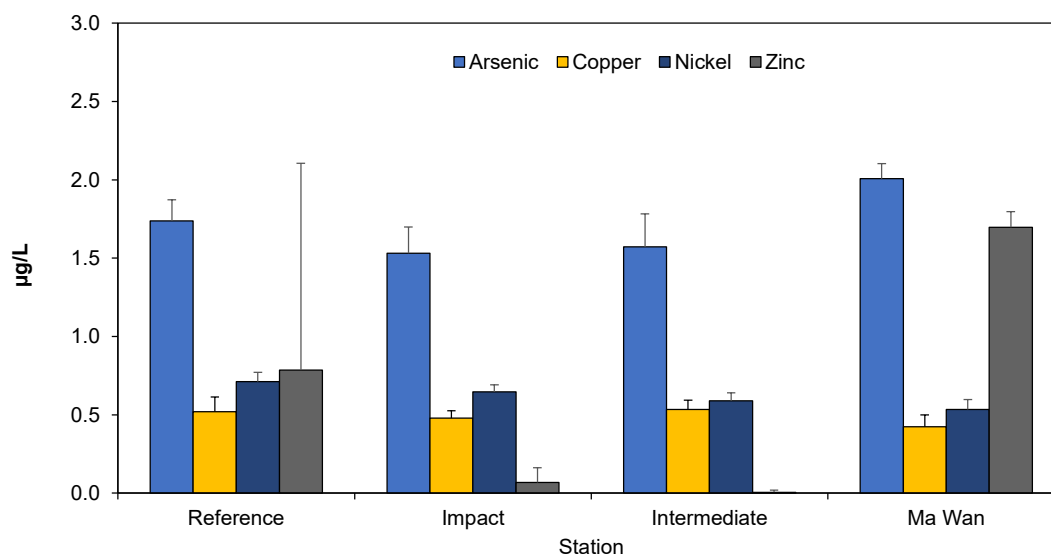


**Figure 7:** Concentration of Arsenic, Copper, Nickel, and Zinc (µg/L; mean + SD) in water samples collected from Routine Water Quality Monitoring for disposal operations at ESC CMP V in February 2023


### Routine Water Quality Monitoring for ESC CMP V February 2023

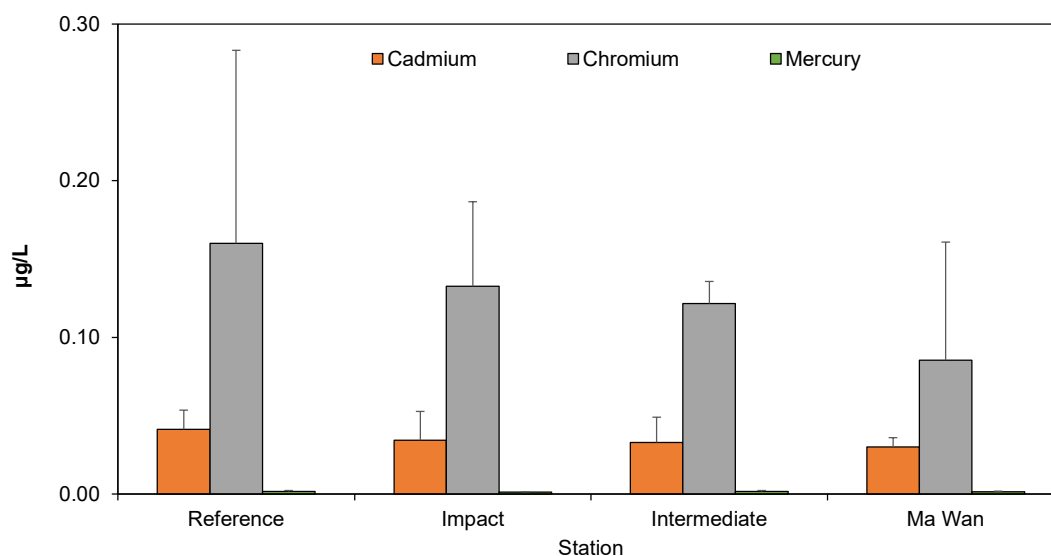

**Figure 8:** Concentration of Cadmium, Chromium, Mercury (µg/L; mean + SD) in water samples collected from Routine Water Quality Monitoring for disposal operations at ESC CMP V in February 2023

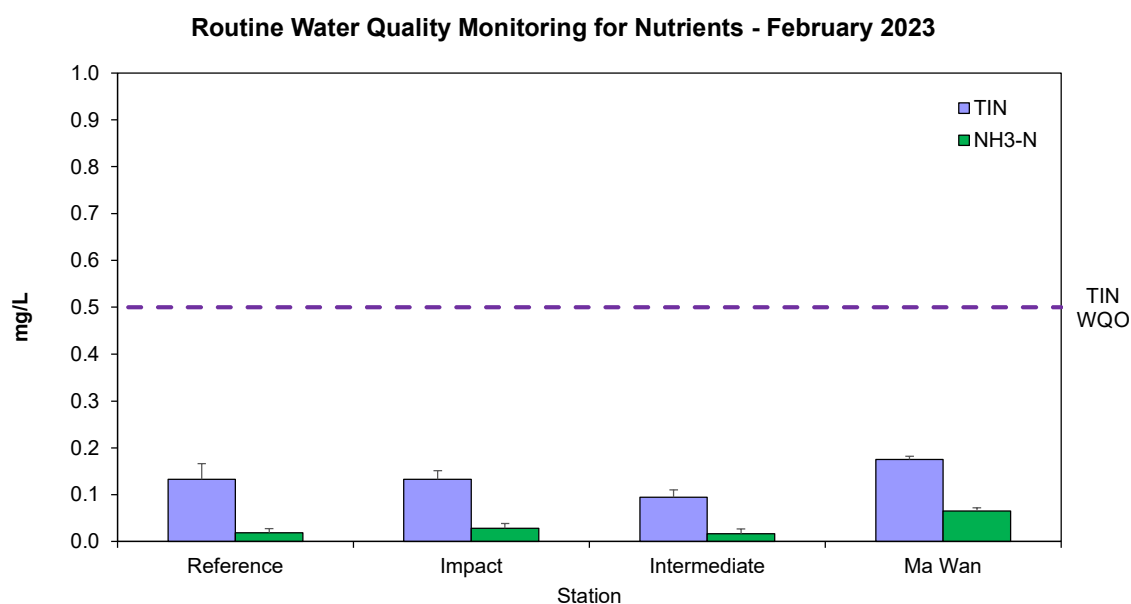


**Figure 9:** Concentration of Total Inorganic Nitrogen (TIN) and Ammonia Nitrogen (NH3-N) (mg/L; mean + SD) in water samples collected from Routine Water Quality Monitoring for disposal operations at ESC CMP V in February 2023

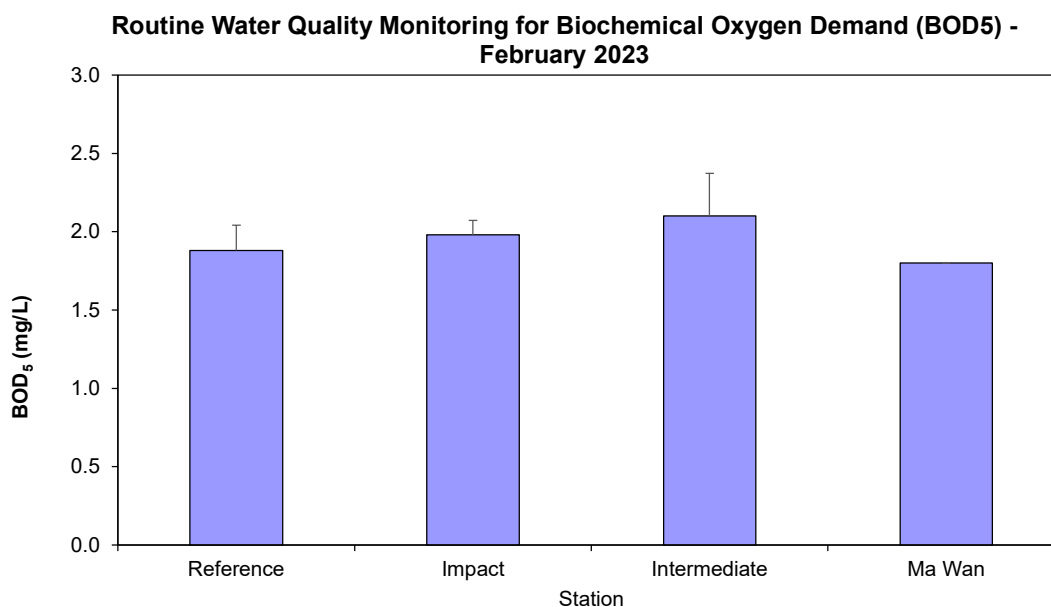


**Figure 10:** Level of Biochemical Oxygen Demand (BOD5) (mg/L; mean + SD) in water samples collected from Routine Water Quality Monitoring for disposal operations at ESC CMP V in February 2023

### Routine Water Quality Monitoring for Suspended Solids - February 2023

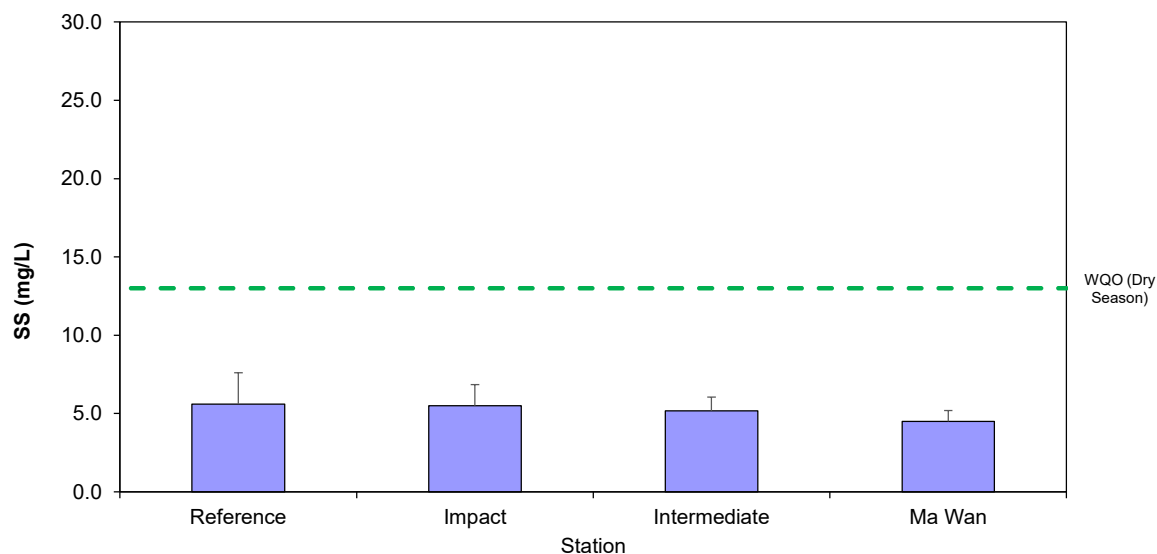


**Figure 11** Concentration of Suspended Solids (SS) (mg/L; mean + SD) in water samples collected from Routine Water Quality Monitoring for disposal operations at ESC CMP V in February 2023


### Pit Specific Sediment Chemistry for Metal and Metalloid Contaminants at ESC CMP Vb - February 2023

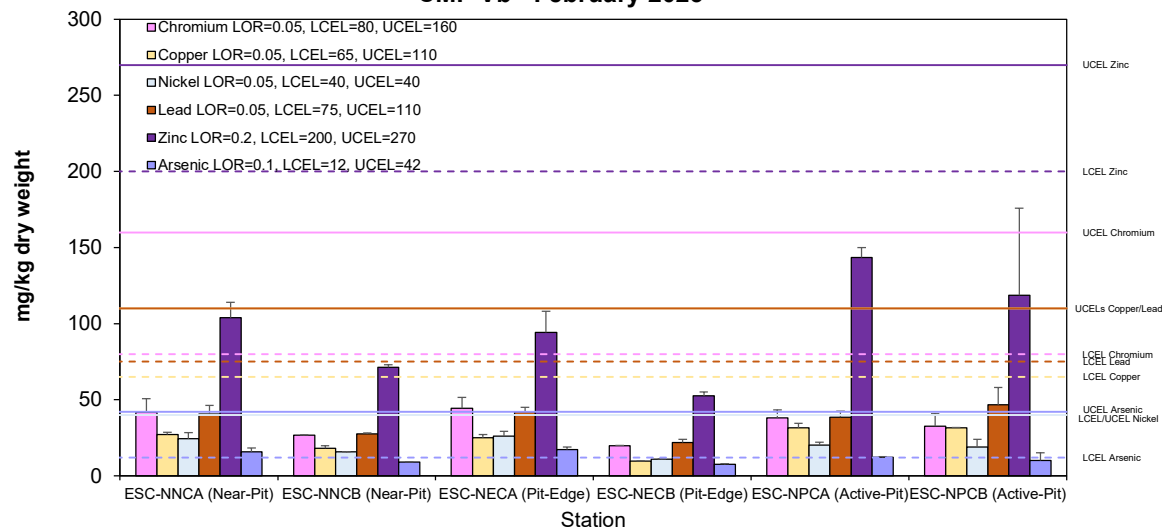

**Figure 12:** Concentration of Metals and Metalloid (Cr, Cu, Ni, Pb, Zn, As; mg/kg dry weight; mean + SD) in sediment samples collected from Pit Specific Sediment Chemistry Monitoring for ESC CMP Vb in February 2023

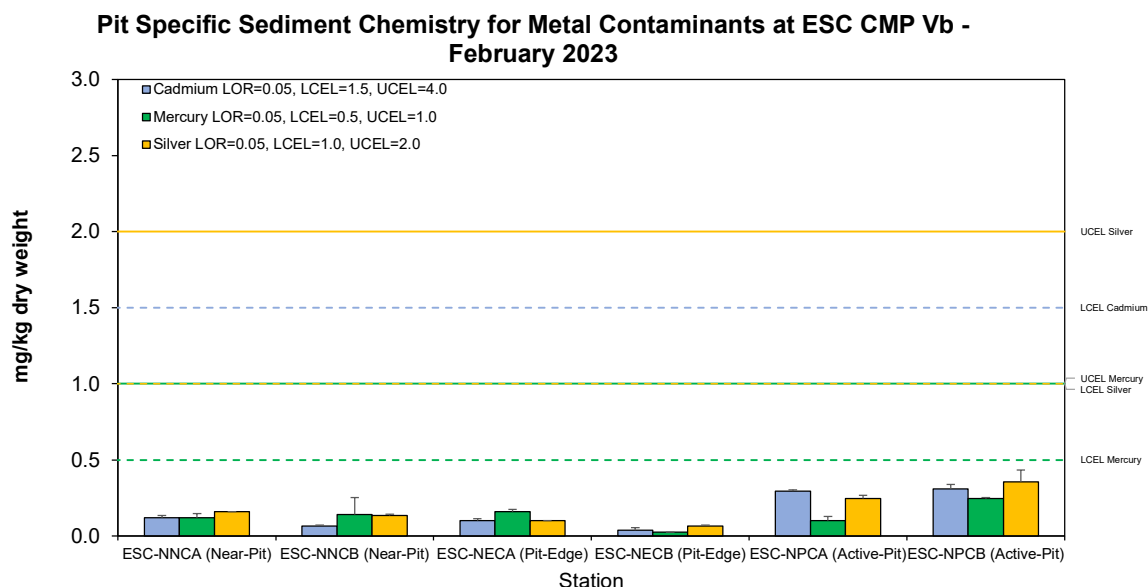


**Figure 13:** Concentration of Metals (Cd, Hg, Ag; mg/kg dry weight; mean + SD) in sediment samples collected from Pit Specific Sediment Chemistry Monitoring for ESC CMP Vb in February 2023

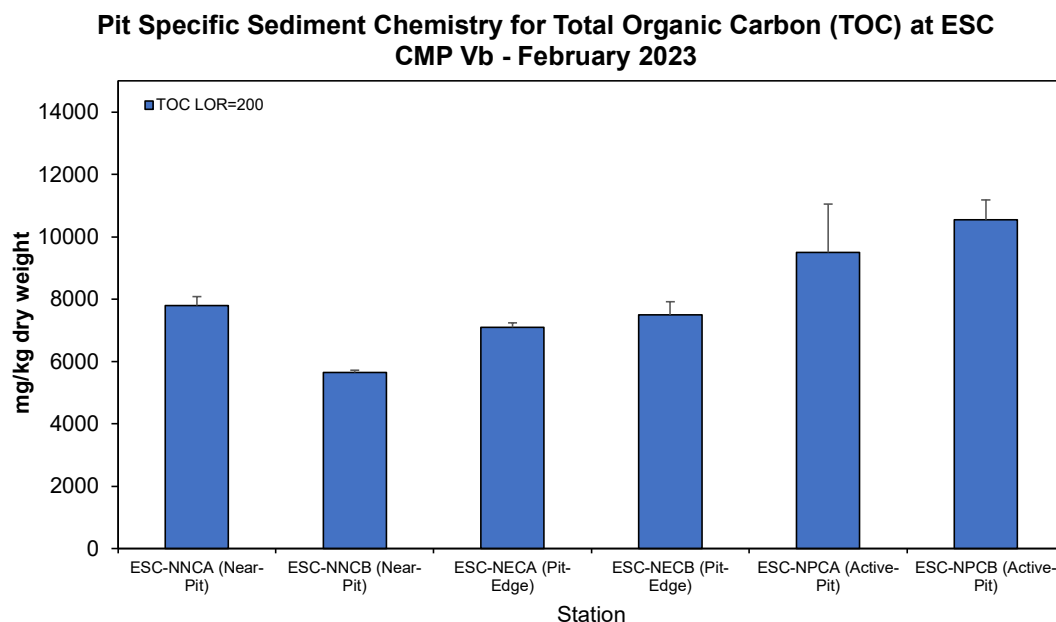


**Figure 14:** Concentration of Total Organic Carbon (TOC) (mg/kg dry weight; mean + SD) in sediment samples collected from Pit Specific Sediment Chemistry Monitoring for ESC CMP Vb in February 2023

**Pit Specific Sediment Chemistry for Low and High Molecular Weight Polycyclic Aromatics Hydrocarbons (PAHs) at ESC CMP Vb - February 2023**  
( 1 of 2 )

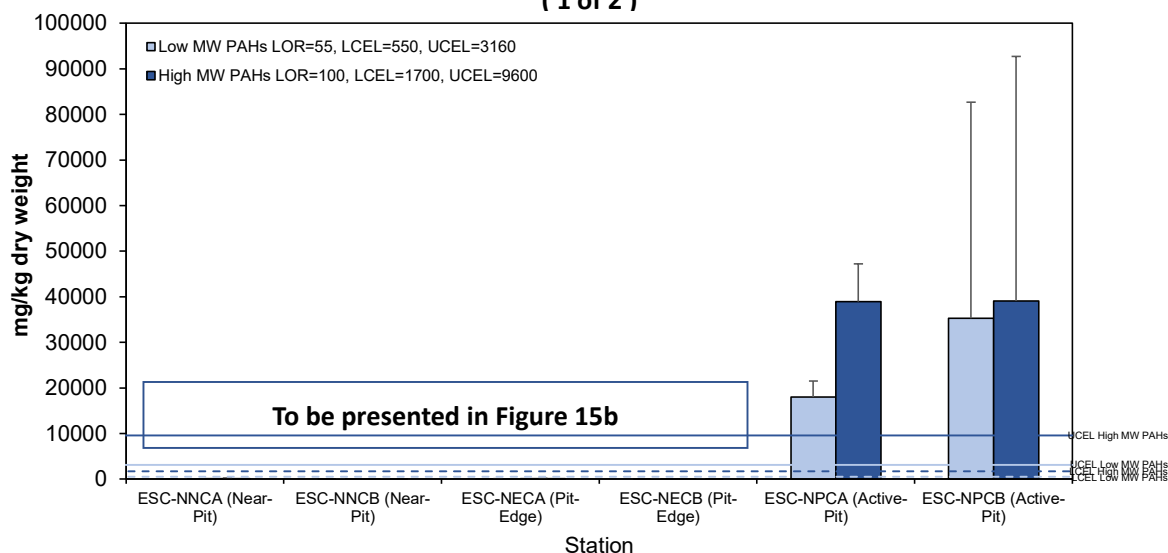

**Figure 15a** Concentration of Low and High Molecular Weight Polycyclic Aromatic Hydrocarbons (mg/kg dry weight; mean + SD) in sediment samples collected from Pit Specific Sediment Chemistry Monitoring for ESC CMP Vb in February 2023


**Pit Specific Sediment Chemistry for Low and High Molecular Weight Polycyclic Aromatics Hydrocarbons (PAHs) at ESC CMP Vb - February 2023**  
( 2 of 2 )

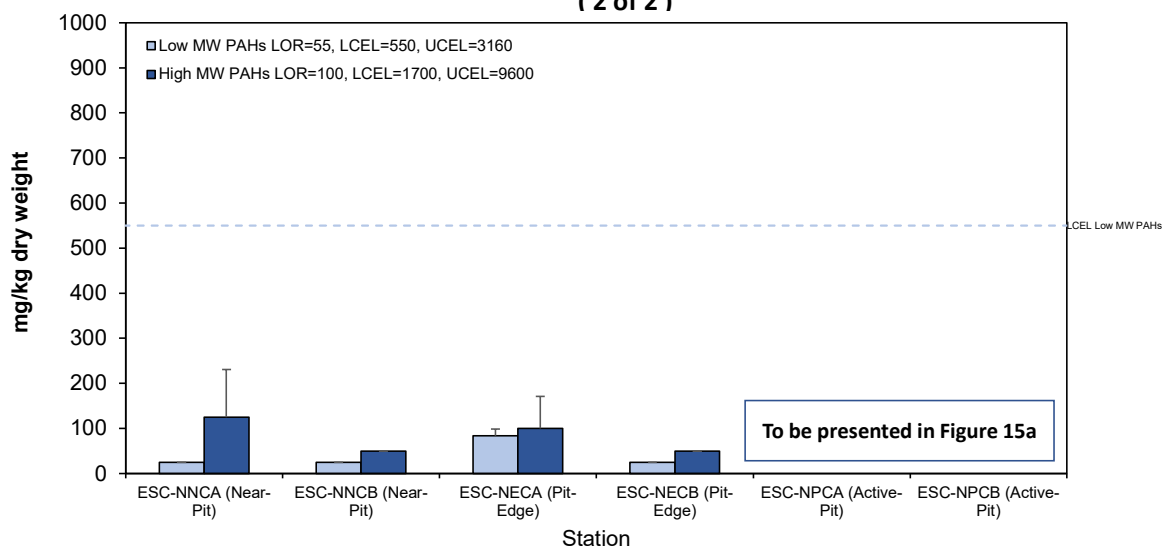

**Figure 15b** Concentration of Low and High Molecular Weight Polycyclic Aromatic Hydrocarbons (mg/kg dry weight; mean + SD) in sediment samples collected from Pit Specific Sediment Chemistry Monitoring for ESC CMP Vb in February 2023




### Cumulative Impact Sediment Chemistry for Metal and Metalloid Contaminants at ESC CMPs - February 2023

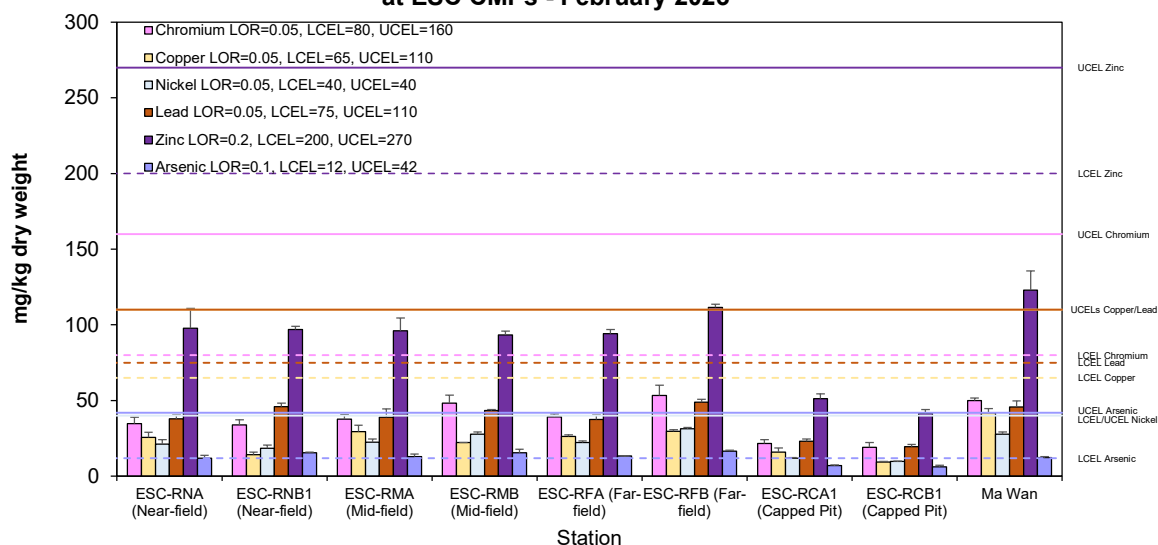


**Figure 16:** Concentration of Metals and Metalloid (Cr, Cu, Ni, Pb, Zn, As; mg/kg dry weight; mean + SD) in sediment samples collected from Cumulative Impact Sediment Chemistry Monitoring for ESC CMPs in February 2023

### Cumulative Impact Sediment Chemistry for Metal Contaminants at ESC CMPs - February 2023

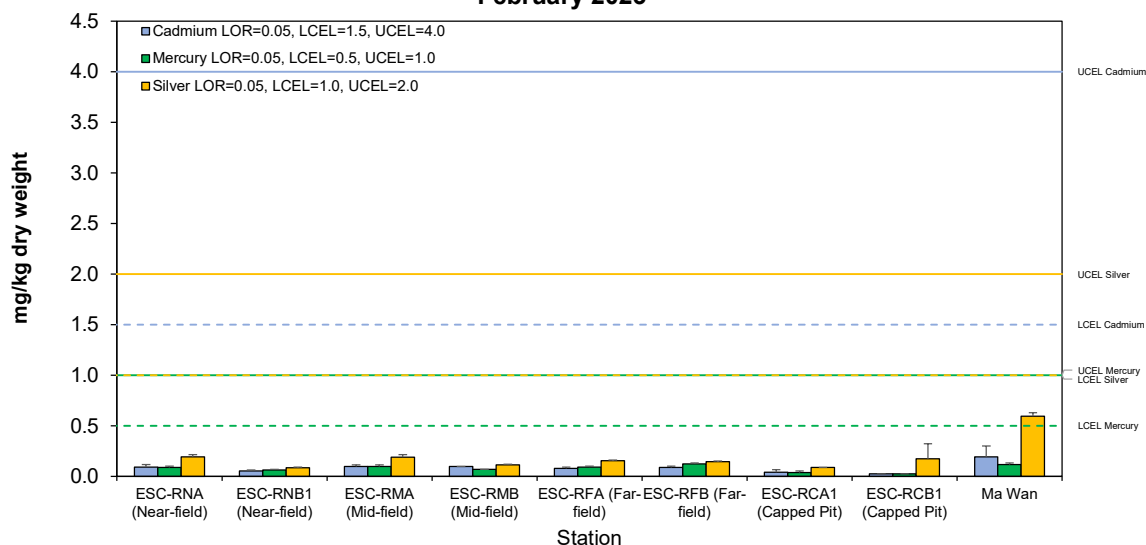


**Figure 17:** Concentration of Metals (Cd, Hg, Ag; mg/kg dry weight; mean + SD) in sediment samples collected from Cumulative Impact Sediment Chemistry Monitoring for ESC CMPs in February 2023

### Cumulative Impact Sediment Chemistry for Total Organic Carbon (TOC) at ESC CMPs - February 2023

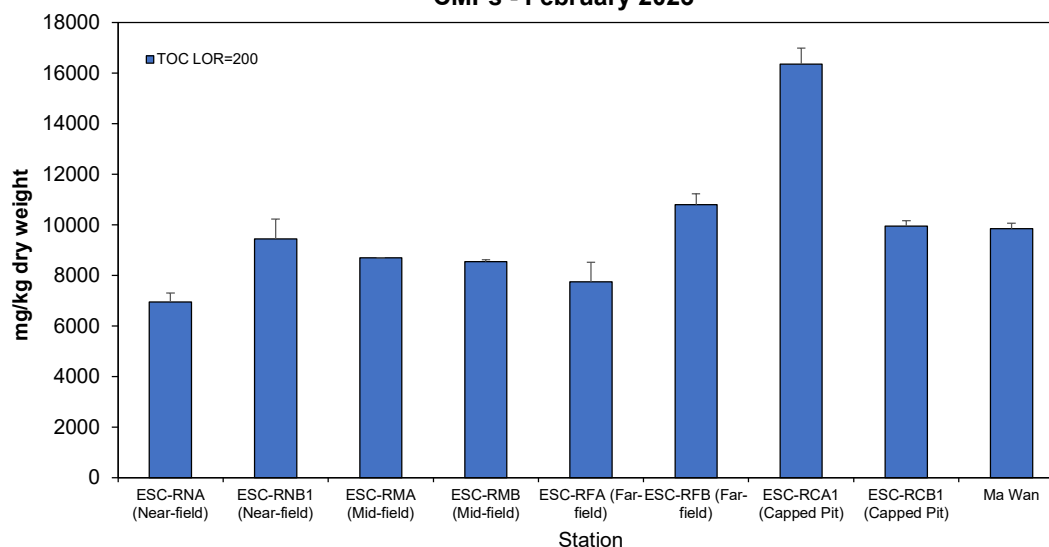


**Figure 18:** Concentration of Total Organic Carbon (TOC) (mg/kg dry weight; mean + SD) in sediment samples collected from Cumulative Impact Sediment Chemistry Monitoring for ESC CMPs in February 2023

### Cumulative Impact Sediment Chemistry for Low and High Molecular Weight Polycyclic Aromatics Hydrocarbons (PAHs) at ESC CMPs - February 2023

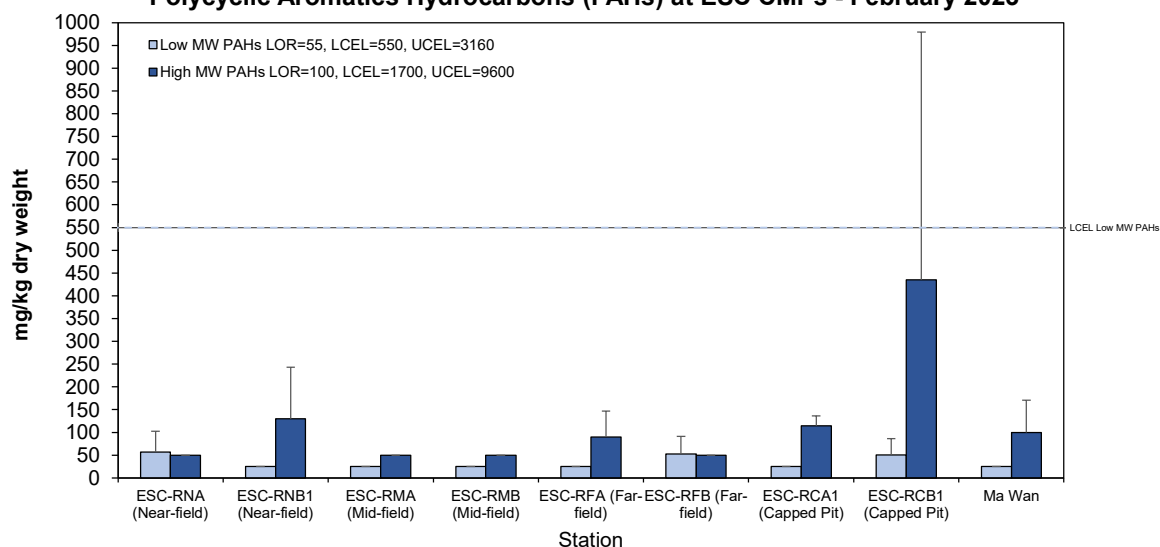

**Figure 19:** Concentration of Low and High Molecular Weight Polycyclic Aromatics (mg/kg dry weight; mean + SD) in sediment samples collected from Cumulative Impact Sediment Chemistry Monitoring for ESC CMPs in February 2023

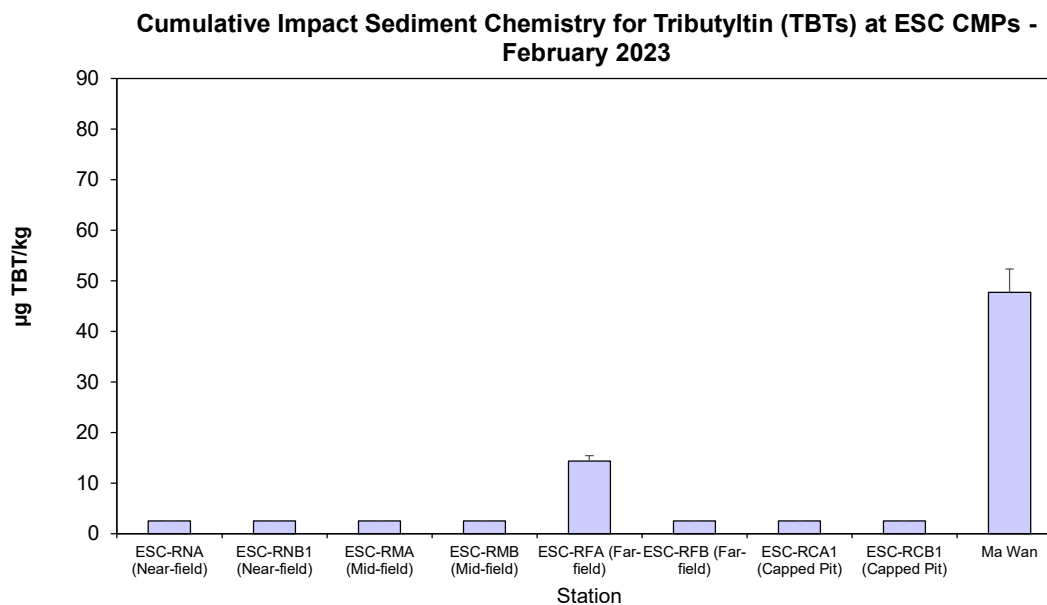

**Figure 20:** Concentration of Tributyltin (TBT) (µg/kg dry weight; mean + SD) in sediment samples collected from Cumulative Impact Sediment Chemistry Monitoring for ESC CMPs in February 2023

## Appendix D. Study Programme

# Study Programme

## Agreement No. CE 59/2020 (EP) Environmental Monitoring and Audit for Disposal Facility to the East of Sha Chau (2021-2026) - Investigation

Mott MacDonald Hong Kong Limited

| ID  | Task Name                                                                                              | Start    | Finish   | 202120222023202420252026 |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|-----|--------------------------------------------------------------------------------------------------------|----------|----------|--------------------------|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|
|     |                                                                                                        |          |          | 1                        | 2 | 3 | 4 | 1 | 2 | 3 | 4 | 1 | 2 | 3 | 4 | 1 | 2 | 3 | 4 | 1 | 2 | 3 | 4 | 1 | 2 | 3 |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 1   | COMMENCEMENT OF AGREEMENT NO. CE 59/2020 (EP)                                                          | 01/04/21 |          | ◆                        |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 2   | EAST OF SHA CHAU CONTAMINATED MUD PITS (ESC CMPs) BETWEEN 2021 & 2026                                  | 01/04/21 | 25/06/26 | ◆                        |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 3   | Draft Report of First Review of EM&A Manual (for ESC CMPs)                                             |          | 30/04/21 | ◆                        |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 4   | Final Report of First Review of EM&A Manual (for ESC CMPs)                                             |          | 20/05/21 | ◆                        |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 5   | Draft Report of Subsequent Review of EM&A Manual (for ESC CMPs) - annual basis assumed                 | 30/04/22 | 30/04/25 | ◆                        |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 10  | Final Report of Subsequent Review of EM&A Manual (for ESC CMPs) - annual basis assumed                 | 20/05/22 | 20/05/25 | ◆                        |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 15  | Regular Site Inspections of CMP Contractors                                                            | 01/04/21 | 31/03/26 | ◆                        |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 16  | Monthly EM&A Report                                                                                    | 14/05/21 | 14/04/26 | ◆                        |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 77  | Quarterly EM&A Report                                                                                  | 30/07/21 | 30/04/26 | ◆                        |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 98  | Annual EM&A Report                                                                                     | 30/01/22 | 30/01/26 | ◆                        |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 104 | Annual Risk Assessment Report                                                                          | 31/05/22 | 31/05/26 | ◆                        |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 110 | Draft Final Report                                                                                     |          | 30/04/26 | ◆                        |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 111 | Final Report                                                                                           |          | 04/06/26 | ◆                        |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 112 | Draft Executive Summary                                                                                |          | 04/06/26 | ◆                        |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 113 | Final Executive Summary                                                                                |          | 25/06/26 | ◆                        |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 114 | EAST OF TUNG LUNG CHAU (ETLC) DISPOSAL FACILITY (MONITORING PERIOD: SEPTEMBER 2021 & MARCH-APRIL 2022) | 23/11/21 | 31/08/22 | ◆                        |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 115 | Monthly EM&A Report                                                                                    | 23/11/21 | 06/06/22 | ◆                        |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 119 | Quarterly EM&A Report                                                                                  | 15/07/22 | 15/07/22 | ◆                        |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 121 | Annual EM&A Report                                                                                     | 31/08/22 | 31/08/22 | ◆                        |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |

Programme Revision: C  
Date: 11/05/22

Start/End of ET Services

Location

Repeating Task

Start of Agreement

Submission

Multiple-Occasion Submission

